BUSINESS BANK · BUSINESS BANKING TRANSFORMATION OFFICE

Business Lending Process Redesign ahead of the BLP Replacement Programme

Phase 0 – Mobilise
Deliverables 0.1 to 0.10

Project code	BB-BLP-BPR
Document set	Phase 0 deliverables for G0 approval
Version	1.0
Engagement start	Monday 9 November 2026 (Week 1)
Gate	G0 – SteerCo, Week 2
Prepared by	Engagement Manager

Contents

#	Deliverable	Owner	Accepted by
0.1	Project Charter	Engagement Lead	SteerCo
0.2	Governance Pack	PMO	SteerCo
0.3	Integrated Project Plan and Resource Plan	PMO	SteerCo
0.4	RAID Log	PMO	Project leadership; SteerCo
0.5	Stakeholder Map, Engagement Plan and Communications Plan	WS5 People & Change	Business Owner
0.6	Hypothesis Tree and Discovery Mapping	WS1 Journeys & Process	Design Authority
0.7	Data Request and Data Provisioning Plan	WS3 Data & MI	Head of MI & Regulatory Reporting
0.8	Replacement Programme Dependency Map and Joint Decision Log	WS4 Technology	Replacement Programme Director
0.9	Benefits Logic Tree	WS6 PMO & Benefits	Finance Director
0.10	Kick-off Deck	Engagement Lead	Sponsor

Reading order. 0.1 and 0.2 set what the project is and who decides. 0.3 and 0.4 set when and what could go wrong. 0.5 to 0.9 are the working instruments for Phase 1. 0.10 is the kick-off presentation that asks the SteerCo for the G0 decisions.

Cross-references. Scope decisions SD-01 to SD-04 (0.1) · Risks R-01 to R-13 (0.4) · Data items DR-01 to DR-18 (0.7) · Design decisions DD-01 to DD-10 (0.8) · Levers L1 to L15 and benefits BN-01 to BN-12 (0.9) · Hypotheses A1 to F2 (0.6).

0.1 Project Charter

Business Lending Process Redesign ahead of the BLP Replacement Programme

Project code	BB-BLP-BPR
Version	1.0 – for G0 approval
Prepared by	Engagement Manager
Approved by	SteerCo (G0, Week 2)
Engagement start	Monday 9 November 2026 (Week 1)

1. Purpose of this charter

This charter is the single reference for what the project is, what it is not, how success is judged, and who decides. It is approved once at G0. Any change after G0 goes through change control (§11) and is recorded in the decision log, so that scope is not re-opened informally at later gates.

2. Background

Business Bank administers c. 30,500 business lending deals a year across 12 product families on the Business Lending Platform (BLP), used by c. 900 colleagues from Business Direct to Corporate. BLP is being replaced. The Bank has produced current-state journey maps for the replacement but has not yet defined a target-state process. Without one, the replacement will be configured to today's process, including its workarounds (Blue Prism bots, four batch jobs, off-platform facility letters) and its redundant deal types.

This project defines the target-state lending process, operating model and business case, and delivers a process requirements pack to the BLP Replacement Programme before its requirements baseline is frozen.

3. Objectives and success criteria

#	Objective	Success criterion at G2 (design approved)	Success criterion at benefits realisation
O1	Reduce time to decision and fulfilment, with priority on servicing journeys	Target cycle time per journey pattern set against the G1 baseline and accepted by SteerCo	Target cycle times achieved in pilot segment within 2 releases
O2	Reduce cost to serve and release capacity	Capacity release by role quantified, with named benefit owners	≥ 80% of signed benefit realised within 12 months of each release
O3	Maintain or strengthen credit control	Every removed or automated control has a signed control-equivalence entry; zero unresolved second-line objections	No increase in policy exceptions or authority breaches post-implementation
O4	Reduce rework	Rework loops identified, quantified and designed out or bounded	First-time-right rate improved against baseline by the agreed target
O5	Simplify for the replacement	Deal types reduced to agreed journey patterns; Fit/Configure/Custom/Gap classification complete; requirements pack accepted into Programme backlog	Custom build on the replacement limited to items on the approved custom list
O6	Protect regulatory and MI data	No regulatory reporting field removed without MI sign-off; data lineage documented	No regulatory reporting break at go-live
O7	Improve colleague and customer experience	RM steps per journey reduced; measurement approach agreed	RM and customer measures improved against baseline

Headline target to be confirmed at G1 (indicative ranges only, from industry benchmarks, not yet from Bank data): 30–50% reduction in end-to-end cycle time on fast-track renewals; 15–25% touch-time reduction across servicing journeys; deal types reduced from 11 to 5 patterns.

4. Scope

4.1 In scope

- Lending lifecycle processes administered on BLP: lead and opportunity, deal and credit, documentation and fulfilment, in-life servicing (Renewal, EPR, Variation, Remove All Facilities, change after approval), distressed handling (CAP Referral, CAP Strategy, in-flight referral), pre-approved drawdown (Shadow Limit, Shadow Limit Reallocation, Staged Drawdown, Staged Drawdown Allocation)
- Deposit opportunity recording
- All 12 product families; all 11 deal types including retirement decisions
- Segments: Business Direct, Strategic Finance, Corporate (depth per §5)
- Controls, delegated-authority rules and policy application embedded in the processes
- Workarounds around BLP: Blue Prism bots, the four batch jobs, off-platform documents, email issuance
- Roles: RMs, Business Direct, Credit, Lending Services, Fulfilment, SBS/PS, Business Operations, Corporate Associates, Credit Risk Policy, MI/Regulatory Reporting

4.2 Out of scope

- Personal Association Lend
- Platform selection, build, configuration, testing, data migration
- Credit policy content and risk appetite (application and controls are in scope; policy setting is not)
- Changes to MEO, IMPACS, TELLER, CIF Portal beyond interface requirements
- Personal lending; retail deposits

5. Scope decisions for G0

These four were left open in the RFP. The recommendation is recorded here; the SteerCo decision is recorded in the decision log (0.8) at G0.

ID	Decision	Options	Recommendation	Rationale
SD-01	ESR Cleanse (12.5% of volume)	(a) In scope as a process; (b) Out of scope, handled by Replacement data migration; (c) In scope only to specify what migration must preserve	**(c)**	It is a records transfer, not a customer deal. Keeping it in the deal list distorts volumes and the baseline. The project should specify the personal-exposure and NAG-exposure updates migration must preserve, then stop.
SD-02	Corporate segment depth	(a) Full mapping and baselining; (b) Mapping only, via Corporate Associates as proxies, no restricted data; (c) Exclude	**(b)**	Insider-information barriers prevent partner access to live Corporate data. Journeys are structurally the same; segment differences can be captured through proxies without restricted data.
SD-03	Deposit opportunity location	(a) Stays on lending platform; (b) Moves to CRM/pipeline tool; (c) Defer until Replacement platform's opportunity capability is confirmed	**(c), decide by G1**	98 opportunities in progress is low volume; the right home depends on whether the replacement has a usable opportunity object. Deciding now risks a wrong answer.
SD-04	Capacity release treatment	(a) Headcount reduction target; (b) Redeployment to revenue activity; (c) Quantify capacity only; treatment decided by line management post-G2	**(c)**	Keeps the project credible with RMs and Credit during discovery (participation collapses if the project is seen as a headcount exercise). Business case shows capacity in FTE-equivalent and value at both treatments.

6. Approach summary

Five phases, four gates. Detail in the Approach document (02) and the Integrated Plan (0.3).

Phase	Weeks	Gate	Gate decision
0 Mobilise	1–2	G0	Charter, governance, plan approved
1 Discover	3–7	G1	Baseline endorsed as the reference for benefits
2 Design	8–13	G2	To-be design and business case approved; funding released; requirements pack accepted by Replacement Programme

Phase	Weeks	Gate	Gate decision
3 Plan Delivery	14–17	G3	Ready to implement
4 Implement, Embed, Track	18+	per release	Scale / no-scale per pilot and release

Design principles that bind the approach: fit-to-standard against the replacement platform; no control removed without equivalence; route by risk not by deal type; capture once at source.

7. Key deliverables and acceptance

Phase	Deliverable	Accepted by
0	Charter, governance pack, plan, RAID, stakeholder and comms plan, hypothesis tree, data request, dependency map and decision log, benefits logic tree, kick-off	SteerCo
1	Validated as-is maps, deal type × stage matrix, performance and effort baseline, control inventory, workaround inventory, data lineage, pain-point and root-cause register, sized opportunity list, current-state report	SteerCo (baseline); Credit Risk (control inventory); MI (data lineage)
2	Design principles, journey patterns, to-be maps, routing design, control equivalence, gap analysis, fit-gap, requirements pack, TOM and RACI, data design, KPIs, business case, roadmap, sign-off pack	Design Authority; second-line Risk (control equivalence); Replacement Programme (requirements pack); SteerCo (business case)
3	Implementation roadmap, pilot and rollout plan, change impact and TNA, policy change list, benefits plan, delivery governance, artefact handover	SteerCo; line management (change plan)
4	Quick-win report, design assurance per release, pilot evaluation, monthly benefits report, closure report	SteerCo; benefit owners

8. Governance summary

- **Executive Sponsor:** Managing Director, Business Banking
- **Business Owner:** Head of Lending Operations
- **SteerCo:** fortnightly; chaired by Sponsor; decision body for gates and scope
- **Design Authority:** weekly in Phase 2; chaired by Business Owner; includes Head of Credit Risk Policy, second-line Risk, Head of MI & Regulatory Reporting, Replacement Programme Architect
- **Working groups:** one per journey pattern in Phase 1–2, plus Controls and Data
- **Escalation:** Working group → Engagement Manager and Bank PM → Design Authority → SteerCo → Sponsor

Full terms of reference in 0.2.

9. Team and resourcing

Partner team: Engagement Lead (part time), Engagement Manager, BPR/TOM Lead, Credit Risk and Controls Specialist, 2 Lending Process SMEs, Data/MI Analyst, Platform/Integration Analyst, Change Lead (from Phase 2), PMO Analyst.

Bank team: Bank Project Manager and Business Analyst (full time from Week 1), SMEs per role (hours in 0.3), Design Authority members, MI data provider.

10. Assumptions and constraints

Assumptions

- Replacement platform selected, or selected by G1, so fit-gap is against a real product
- Current L3 maps available in editable form in Week 1
- BLP stage-transition timestamps extractable for the last 12 months
- Replacement Programme requirements freeze date is no earlier than Week 13; if earlier, see RAID R-01

Constraints

- No disruption to live lending operations; SME load agreed with line management
- Insider-information barriers for Corporate
- Regulatory reporting fields are protected
- MI data lead time 3–4 weeks

11. Change control

Changes to scope, objectives, gates or key dates after G0 require a change request to the SteerCo, with impact on plan, resource and benefits stated. Decisions are recorded in the decision log (0.8). Changes within a phase that do not affect scope or dates are agreed by the Engagement Manager and Bank PM and logged.

12. Top risks at charter

ID	Risk	Mitigation
R-01	Replacement requirements freeze before G2	Freeze date in writing at G0; interim design decisions released Week 10
R-02	MI extract late or incomplete	Data request issued Week 1; independent survey and time-and-motion baseline
R-03	Late objection from Credit Risk or second line	Both on Design Authority from Week 2; incremental control-equivalence review
R-04	SME availability	Workshop load agreed at G0; scheduled around month-end
R-05	Discovery perceived as a headcount exercise	SD-04 adopted; sponsor message in kick-off

Full register in 0.4.


13. Sign-off

Role	Name	Signature	Date
Executive Sponsor, MD Business Banking			
Business Owner, Head of Lending Operations			
Head of Credit Risk Policy			
Replacement Programme Director			
Engagement Lead (partner)			

0.2 Governance Pack

Project	BB-BLP-BPR
Version	1.0 – for G0 approval
Owner	PMO

1. Governance structure

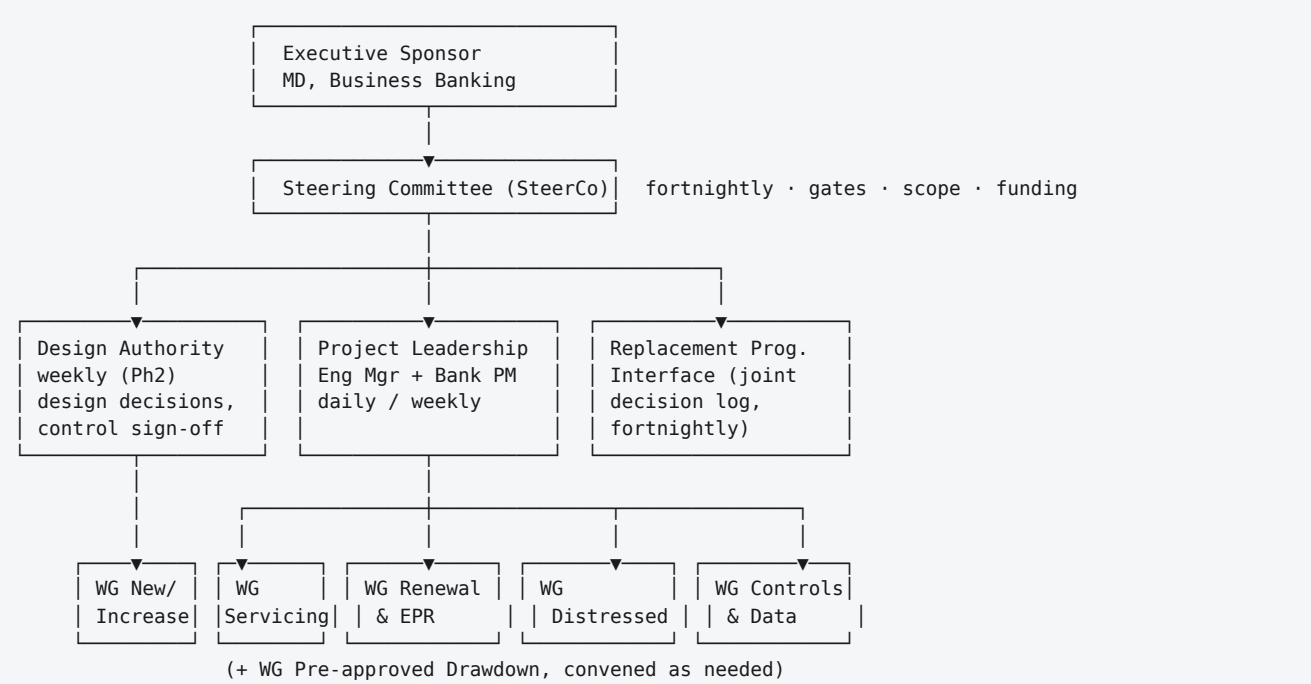

2. Steering Committee – Terms of Reference

Purpose. Own the project outcome. Approve gates, scope changes, the baseline, the design and the business case. Resolve escalations that cross functional lines. Release funding.

Membership

Role	Member	Voting
Chair	MD, Business Banking (Executive Sponsor)	Yes
Business Owner	Head of Lending Operations	Yes
Credit	Chief Credit Officer or Head of Credit Risk Policy	Yes
Risk	Head of Operational Risk (second line)	Yes
Technology	Replacement Programme Director	Yes
Finance	Business Banking Finance Director	Yes
Front line	Head of Business Direct; Head of Strategic Finance	Yes
Partner	Engagement Lead	Advisory
Secretary	PMO	–
Attending	Engagement Manager, Bank PM	–

Cadence. Fortnightly, 60 min, starting Week 2. Gate meetings extended to 90 min. Quorum: Chair (or delegate), Business Owner, Credit, Risk, Technology.

Decision rights

- Approve gates G0–G3 and scale/no-scale decisions in Phase 4
- Approve scope changes and change requests
- Endorse the Phase 1 baseline as the reference for benefits
- Approve the business case and release funding
- Resolve escalations not resolved at Design Authority

Standing agenda. Decisions required · Gate status · Progress vs plan (RAG by workstream) · Top risks and issues · Replacement Programme dependency status · Benefits status (from Phase 2) · AOB.

Inputs. SteerCo pack issued 2 working days before. Decision papers use the one-page format: decision required, options, recommendation, impact, owner.

Outputs. Decisions recorded in decision log within 1 working day; actions in action log.

3. Design Authority – Terms of Reference

Purpose. Approve the design: principles, journey patterns, to-be maps, routing criteria, control equivalence, data design and the requirements pack. Ensure the design is deliverable on the replacement platform and acceptable to Credit Risk, second line and MI.

Membership

Role	Member	Sign-off responsibility
Chair	Head of Lending Operations	Overall design
Credit Risk Policy	Head of Credit Risk Policy	Routing criteria; policy application
Second-line Risk	Senior Operational Risk Manager	Control equivalence
MI and Regulatory Reporting	Head of MI & Reg Reporting	Data lineage; protected fields
Replacement Programme	Solution Architect	Fit-gap; requirements pack deliverability
Front line	Senior RM (Strategic Finance); Business Direct Team Leader	Workability
Operations	Head of Lending Services; Head of Fulfilment	Workability
Partner	BPR/TOM Lead; Credit Risk and Controls Specialist	Presenting
Secretary	PMO	–

Cadence. Fortnightly in Phase 1 (from Week 4); weekly in Phase 2; fortnightly in Phase 3; per release in Phase 4. 90 min.

Decision rights. Approve design artefacts listed above. Cannot change scope or objectives (SteerCo). Cannot waive a control without second-line signature. Disagreements not resolved in two sittings escalate to SteerCo.

Rule for control changes. No to-be map is approved while it contains an eliminated or automated control without a corresponding entry in the control equivalence register signed by second line.

4. Working groups

WG	Scope	Lead (partner)	Lead (Bank)	Members	Cadence
New/Increase	New Money, Increase	Lending SME 1	Senior RM	RM, Credit, Lending Services, Fulfilment	Weekly Ph1–2
Servicing	Variation, Remove All Facilities, change after approval	Lending SME 2	Business Ops Lead	RM, Credit, Lending Services, Business Ops	Weekly Ph1–2
Renewal & EPR	Renewal, EPR	BPR/TOM Lead	Business Direct Team Leader	RM, Business Direct, Credit, Corporate Associate	Weekly Ph1–2

WG	Scope	Lead (partner)	Lead (Bank)	Members	Cadence
Distressed	CAP Referral, CAP Strategy, in-flight referral	Lending SME 1	Head of SBS	SBS/PS, Credit, RM	Fortnightly
Pre-approved Drawdown	Shadow Limit, Reallocation, Staged Drawdown Allocation	Lending SME 2	Senior RM	RM, Credit, Fulfilment	As needed
Controls & Data	Control inventory, equivalence, data lineage, MI	Credit Risk and Controls Specialist; Data/MI Analyst	Credit Risk Policy Manager; MI Manager	Second line, MI, Reg Reporting	Weekly

5. Project leadership

Engagement Manager and Bank PM meet daily (15 min stand-up) and weekly (60 min plan and RAID review). Workstream leads attend the weekly. Weekly status report issued Friday to Sponsor, Business Owner and Replacement Programme Director.

6. Replacement Programme interface

Joint fortnightly 45-min session: Engagement Manager, Platform/Integration Analyst, Programme Manager, Solution Architect. Owns the joint decision log (0.8), the freeze date, and the interim design-decision releases. Replacement Programme Director sits on SteerCo; Solution Architect sits on Design Authority.

7. Escalation path

Level	Forum	Resolution time
1	Working group	Within the meeting
2	Engagement Manager and Bank PM	2 working days
3	Design Authority (design) / Project Leadership (delivery)	Next sitting
4	SteerCo	Next sitting or extraordinary
5	Executive Sponsor	2 working days

8. Decision log format

ID	Date	Forum	Decision required	Options considered	Decision	Rationale	Owner	Status

Maintained by PMO. Decisions are not revisited unless a change request is raised with new information.

9. Governance calendar (Weeks 1–17)

Week	SteerCo	Design Authority	Replacement interface	Working groups
1	–	–	Dependency session	–
2	**G0**	–	–	–
3	–	–	✓	Launch all
4	✓	✓ (fortnightly)	–	✓
5	–	–	✓	✓
6	✓	✓	–	✓
7	**G1**	–	✓	✓
8	–	✓ (weekly from here)	–	✓
9	✓	✓	✓	✓
10	–	✓	✓ (interim design release)	✓

Week	SteerCo	Design Authority	Replacement interface	Working groups
11	✓	✓	–	✓
12	–	✓ (design sign-off)	✓	✓
13	**G2**	–	✓ (requirements pack handover)	–
14	–	✓ (fortnightly)	–	–
15	✓	–	✓	–
16	–	✓	–	–
17	**G3**	–	✓ (artefact handover)	–

10. RACI for governance decisions

Decision	Sponsor	SteerCo	Design Authority	Eng Mgr / Bank PM	Credit Risk	2nd line	Repl. Programme
Gate approval	A	R	C	R	C	C	C
Scope change	A	R	C	R	C	I	C
Baseline endorsement	I	A/R	C	R	C	I	I
Design principles	I	I	A/R	R	C	C	C
To-be maps	I	I	A/R	R	C	C	C
Routing criteria	I	I	A	R	R	C	I
Control equivalence	I	I	A	R	C	R	I
Requirements pack	I	I	A	R	I	I	R (accept)
Business case	A	R	C	R	C	I	C

0.3 Integrated Project Plan and Resource Plan

Project	BB-BLP-BPR
Version	1.0 – baseline at G0
Week 1	w/c Monday 9 November 2026
Owner	PMO

1. Milestones

ID	Milestone	Week	Date (w/c)	Gate
M01	Engagement start; data request issued; Replacement dependency session held	1	9 Nov 2026	
M02	Scope decisions SD-01–04 made; charter approved	2	16 Nov 2026	**G0**
M03	Working groups launched; taxonomy agreed	3	23 Nov 2026	
M04	MI extract received	4–5	30 Nov – 7 Dec	
M05	Activity survey complete	5	7 Dec 2026	
M06	As-is maps validated, exception paths mapped	6	14 Dec 2026	
M07	Baseline endorsed	7	21 Dec 2026	**G1**
–	Christmas / New Year reduced capacity	–	28 Dec – 1 Jan	
M08	Design principles and journey patterns approved	8	4 Jan 2027	
M09	Interim design decisions released to Replacement Programme	10	18 Jan 2027	
M10	Design Authority sign-off of to-be design and control equivalence	12	1 Feb 2027	
M11	Business case approved; requirements pack handed over	13	8 Feb 2027	**G2**
M12	Pilot plan and benefits baseline frozen	16	1 Mar 2027	
M13	Ready to implement; artefact handover	17	8 Mar 2027	**G3**

Note: Week 7 (G1) lands the week before Christmas. If SteerCo availability is a problem, G1 moves to Week 8 (4 Jan) and Phase 2 compresses by a week; see RAID R-08.

2. Plan by workstream

Legend: ■ active · ▲ milestone/gate

Workstream / activity	W1	W2	W3	W4	W5	W6	W7	W8	W9	W10	W11	W12	W13	W14	W15	W16	W17
Gates		▲G0					▲G1						▲G2				▲G3
WS1 Journeys & Process																	
Hypothesis tree	■	■															
Taxonomy L1–L2, inventory			■														
Deal type × stage matrix			■	■	■												
Journey validation workshops (12–14)			■	■	■												
Exception-path mapping				■	■	■											

Workstream / activity	W1	W2	W3	W4	W5	W6	W7	W8	W9	W10	W11	W12	W13	W14	W15	W16	W17
Walk-the-process (5 days)				■	■												
Pain points, root cause, long-list						■	■										
Current-state report							■										
Design principles, patterns								■									
To-be maps per pattern								■	■	■	■						
Exception-path and letter design									■	■	■						
Gap analysis											■	■					
Pilot and rollout plan														■	■		
WS2 Controls																	
Control and DA inventory			■	■	■	■											
Routing criteria with Credit Risk								■	■	■							
Control equivalence register									■	■	■	■					
Policy/procedure change list														■	■		
WS3 Data & MI																	
Data request, provisioning	■	■	■	■													
Cycle-time and volume analysis				■	■	■											
Activity survey (design, run, analyse)			■	■	■	■											
Time-and-motion (top 5 activities)					■	■											
Cost per deal, effort baseline						■	■										
Data lineage				■	■	■											
Data and MI design; KPI definitions									■	■	■	■					
Benefits plan, dashboard spec														■	■	■	
WS4 Technology & Replacement interface																	
Dependency map, decision log	■	■															

Workstream / activity	W1	W2	W3	W4	W5	W6	W7	W8	W9	W10	W11	W12	W13	W14	W15	W16	W17
Workaround inventory				■	■	■											
Fit-gap workshops									■	■	■						
Requirements pack										■	■	■	■				
Interim design release										▲							
Tech enablers, effort sizing											■	■					
Artefact handover																■	▲
WS5 People & Change																	
Stakeholder map, comms plan	■	■															
Voice of business interviews			■	■	■												
TOM, RACI, role profiles										■	■	■					
Change impact, TNA														■	■	■	
WS6 PMO & Benefits																	
Plan, RAID, governance set-up	■	■															
Weekly status, SteerCo packs		■	■	■	■	■	■	■	■	■	■	■	■	■	■	■	■
Benefits logic tree	■	■															
Opportunity sizing						■	■										
Business case											■	■	■				
Roadmap, initiative portfolio												■	■	■			

3. Critical path

Data request (W1) → MI extract (W4–5) → cycle-time analysis (W4–6) → baseline (W7, G1) → routing criteria (W8–10) → control equivalence (W9–12) → Design Authority sign-off (W12) → G2 (W13).

Any slip in the MI extract moves G1 directly. Mitigation: activity survey and time-and-motion run independently and can carry G1 with a wider baseline range.

4. Partner resource plan (days per week)

Role	Ph0 (W1–2)	Ph1 (W3–7)	Ph2 (W8–13)	Ph3 (W14–17)	Total days
Engagement Lead	1.5	1	1.5	1	21

Role	Ph0 (W1–2)	Ph1 (W3–7)	Ph2 (W8–13)	Ph3 (W14–17)	Total days
Engagement Manager	5	5	5	5	85
BPR / TOM Lead	5	5	5	5	85
Credit Risk & Controls Specialist	2	4	5	3	66
Lending Process SME 1	2	5	5	2	67
Lending Process SME 2	–	5	5	2	63
Data / MI Analyst	5	5	4	3	71
Platform / Integration Analyst	3	3	5	4	67
Change Lead	–	1	3	5	43
PMO Analyst	5	4	4	4	70

5. Bank resource plan (hours per week)

Role	Ph0	Ph1	Ph2	Ph3	Notes
Executive Sponsor	2	1	2	1	Plus gates
Business Owner	4	3	5	3	Chairs Design Authority
Bank PM	37.5	37.5	37.5	37.5	Full time
Bank BA	37.5	37.5	37.5	37.5	Full time; owns map editing and data liaison
SteerCo members (each)	1	1	1	1	Fortnightly
Design Authority members (each)	–	1	3	1	
Head of Credit Risk Policy	1	3	5	2	Routing criteria co-design
Second-line Risk Manager	1	2	4	1	Control equivalence
MI / Reg Reporting Manager	3	6	3	2	Data extract and lineage
Replacement Solution Architect	2	2	6	3	Fit-gap
Senior RMs (×2)	–	5	3	1	Workshops, shadowing
Business Direct Team Leader	–	5	3	1	
Credit Managers (×2)	–	4	3	1	
Head of Lending Services	–	3	2	1	
Head of Fulfilment	–	3	2	1	
Head of SBS	–	3	2	1	
Corporate Associate	–	2	1	–	Corporate proxy
Activity survey participants (c. 150)	–	1 (W5 only)	–	–	15 min/day for 5 days

6. Workshop schedule (Phase 1)

Week	Workshop	Journey	Attendees	Duration
3	WS-01	Taxonomy and inventory	All WG leads	2 h
3	WS-02	New Money – lead to credit	WG New/Increase	90 min
3	WS-03	New Money – completion and fulfilment	WG New/Increase	90 min
4	WS-04	Renewal and EPR – end to end	WG Renewal	2 h
4	WS-05	Variation – end to end	WG Servicing	2 h
4	WS-06	Remove All Facilities	WG Servicing	90 min
4	WS-07	CAP Referral	WG Distressed	2 h
5	WS-08	CAP Strategy	WG Distressed	90 min

Week	Workshop	Journey	Attendees	Duration
5	WS-09	Shadow Limit and Staged Drawdown (orig.)	WG Pre-approved	90 min
5	WS-10	Shadow Limit Reallocation and Staged Drawdown Allocation	WG Pre-approved	90 min
5	WS-11	Exception paths: decline/appeal/refer, deferral, change after approval	All WGs	2 h
6	WS-12	Security and fulfilment hand-offs	Lending Services, Fulfilment	90 min
6	WS-13	Controls and delegated authority	WG Controls	2 h
6	WS-14	Segment differences (Business Direct / Strategic Finance / Corporate)	Team leaders, Corporate Associate	90 min

7. Plan assumptions

- No workshops in the Christmas fortnight; Phase 2 starts W8 (4 Jan)
- SME hours confirmed by line managers at G0
- MI extract delivered by end W5; later delivery widens baseline range rather than moving G1
- Replacement freeze date no earlier than W13

0.4 RAID Log

Project	BB-BLP-BPR
Version	1.0 – opened at G0
Owner	PMO; reviewed weekly at project leadership, fortnightly at SteerCo

Scoring: Probability 1–5 × Impact 1–5. ≥15 Red, 8–14 Amber, <8 Green.

Risks

ID	Risk	Cause	Effect	P	I	Score	Mitigation	Contingency	Owner	Status
R-01	Replacement Programme freezes requirements before G2	Programme schedule set independently of this project	Target design cannot influence platform configuration; project value drops sharply	3	5	15 R	Freeze date confirmed in writing at G0; interim design-decision release at W10; Programme Director on SteerCo	Prioritise decisions with highest configuration impact (deal types, routing, letters) for early release; accept remaining design as change requests to Programme	Eng Mgr	Open
R-02	MI extract late or incomplete	3–4 week MI lead time; BLP stage timestamps may be partial	Baseline late or weak; G1 slips	4	4	16 R	Data request issued W1; activity survey and time-and-motion run independently	Report baseline as a range at G1; refine in Phase 2	Data/MI Analyst	Open
R-03	Credit Risk or second line reject control changes late in Phase 2	Control implications not visible until to-be maps complete	Design rework; G2 slips	3	5	15 R	Both on Design Authority from W2; control equivalence reviewed incrementally from W9; routing criteria co-designed not presented	Retain contested controls in to-be; record as Phase 4 improvement	Controls Specialist	Open
R-04	SME availability (RMs, Credit) insufficient in Phase 1	Month-end, year-end, live deal pressure	Workshops slip; maps unvalidated	4	3	12 A	Hours agreed with line managers at G0; workshops scheduled off month-end; deputies named	Reduce workshop count by combining journeys with shared stages	Bank PM	Open
R-05	Discovery perceived as a headcount exercise	Capacity-release objective misread	SMEs disengage; survey under-reports touch time	3	4	12 A	SD-04 adopted (capacity quantified, treatment decided post-G2); Sponsor message at kick-off; survey anonymised	Sponsor town-hall; survey re-run with team-leader endorsement	Sponsor	Open

ID	Risk	Cause	Effect	P	I	Score	Mitigation	Contingency	Owner	Status
R-06	Corporate insider-information barriers block discovery	Partner cannot see restricted data	Corporate journeys unvalidated	3	3	9 A	SD-02: Corporate Associates as proxies; Bank BA handles restricted data	Document Corporate as "structurally same, verified by proxy"	BPR Lead	Open
R-07	Design replicates current process on new platform	Familiarity bias; SMEs defend current steps	Objectives O2, O5 missed	3	4	12 A	Design principles signed before mapping; E/A/C/R marking mandatory; fit-to-standard review per step	Design Authority challenge session with external lending SME	BPR Lead	Open
R-08	G1 falls in Christmas week; SteerCo not quorate	Calendar	G1 slips to W8; Phase 2 compresses	4	2	8 A	Confirm SteerCo availability at G0; offer extraordinary session W7 Tuesday	Move G1 to W8; compress Phase 2 by combining W11–12 Design Authority sittings	PMO	Open
R-09	Replacement platform not yet selected by G1	Procurement timing	Fit-gap in Phase 2 is against a generic model, not a product	2	4	8 A	Confirm selection status W1	Fit-gap against the shortlisted products' common capability; re-run for selected product in Phase 3	Platform Analyst	Open
R-10	Benefits disputed at G2	Baseline not owned; benefit owners not named	Funding not released	2	5	10 A	Baseline endorsed at G1; benefit owners named in W11; Finance on SteerCo	Re-base business case on endorsed subset of benefits	Eng Lead	Open
R-11	Activity survey response rate low	900 users, survey fatigue	Touch-time baseline unreliable	3	3	9 A	Sample 15–20%; team-leader sponsorship; 15 min/day; prize-free, anonymised	Extend by one week; rely more on time-and-motion	Data/MI Analyst	Open
R-12	Existing L3 maps not available in editable form	Produced in Visio by Programme; ownership unclear	Re-drawing adds 1–2 weeks	2	3	6 G	Request in W1 from Programme	Redraw from PDF in W3 using Bank BA	Bank BA	Open
R-13	Scope creep into platform build or policy content	Stakeholders use project to raise unrelated issues	Effort diverted	3	2	6 G	Charter §4; parking lot in every workshop; change control	Change request to SteerCo	Eng Mgr	Open

Assumptions

ID	Assumption	Validated by	Date	Status	If false
A-01	Replacement requirements freeze is no earlier than W13	Programme Director, in writing	W1	Open	R-01 contingency

ID	Assumption	Validated by	Date	Status	If false
A-02	BLP stage-transition timestamps extractable for 12 months	MI Manager	W2	Open	R-02 contingency
A-03	Existing L3 maps available in editable form	Programme PM	W1	Open	R-12
A-04	Bank PM and BA assigned full time from W1	Business Owner	W1	Open	Plan slips 1 week per week of delay
A-05	Replacement platform selected by G1	Programme Director	W1	Open	R-09
A-06	Deal volumes in RFP (30,561) are from BLP reporting, consistent with the extract	MI Manager	W4	Open	Re-base volumes
A-07	Line managers will release SMEs for hours in 0.3 §5	Heads of function	G0	Open	R-04
A-08	No material credit policy change is planned during Phases 1–2	Head of Credit Risk Policy	W2	Open	Re-run control inventory

Issues

ID	Issue	Raised	Impact	Action	Owner	Due	Status
I-01	Four current-state maps carry open "TBC" items (repayment schedule per drawdown; associated-party deal updates on Remove All Facilities; off-platform FAL for Shadow Limit and Staged Drawdown; CYB credit card enquiry form as lead source)	W1	As-is incomplete	Resolve in WS-09/10/06 and WS-02	Lending SMEs	W5	Open
I-02	"DO NOT USE" deal type remains selectable in BLP	W1	Data quality; user error	Quick-win candidate: request removal from pick list via BLP change	Bank BA	W3	Open

Dependencies

ID	Dependency	On whom	Needed by	Impact if late	Owner	Status
D-01	Replacement requirements freeze date and backlog access	Replacement Programme	W1	R-01	Platform Analyst	Open
D-02	MI extract per data request (0.7)	MI & Reg Reporting	W5	R-02	Data/MI Analyst	Open
D-03	Editable L3 maps	Replacement Programme	W1	R-12	Bank BA	Open
D-04	Credit policy, delegated-authority matrix, procedure documents	Credit Risk Policy	W3	Control inventory delayed	Controls Specialist	Open
D-05	Blue Prism bot specifications and batch job definitions	Technology / RPA team	W4	Workaround inventory incomplete	Platform Analyst	Open
D-06	Regulatory return specifications sourced from BLP	Reg Reporting	W4	Data lineage incomplete	Data/MI Analyst	Open
D-07	Replacement platform standard lending process documentation	Vendor via Programme	W8	Fit-gap delayed	Platform Analyst	Open
D-08	SME release per resource plan	Heads of function	G0	R-04	Bank PM	Open

0.5 Stakeholder Map, Engagement Plan and Communications Plan

Project	BB-BLP-BPR
Version	1.0 – for G0
Owner	WS5 People & Change


1. Stakeholder register

Influence and interest scored H/M/L. "Current" is our Week 1 read from sponsor interviews; "Required" is where they need to be for the project to succeed.

ID	Stakeholder	Role in project	Influence	Interest	Current stance	Required stance	Key concern	Engagement owner
S-01	MD, Business Banking	Executive Sponsor	H	H	Champion	Champion	Replacement delivers a simpler process; cost to serve	Eng Lead
S-02	Head of Lending Operations	Business Owner; DA Chair	H	H	Supportive	Champion	Operational workability; Lending Services and Fulfilment capacity	Eng Mgr
S-03	Chief Credit Officer / Head of Credit Risk Policy	SteerCo; DA	H	M	Neutral–cautious	Supportive	Fast-track must not weaken control; delegated authority integrity	Controls Specialist
S-04	Head of Operational Risk (2nd line)	SteerCo; DA	H	M	Neutral	Supportive	Control equivalence; audit trail	Controls Specialist
S-05	Replacement Programme Director	SteerCo	H	H	Supportive but schedule-driven	Champion	Freeze date; requirements in usable form	Eng Mgr
S-06	Replacement Solution Architect	DA; fit-gap	M	H	Supportive	Champion	Fit-to-standard; custom build minimised	Platform Analyst
S-07	Business Banking Finance Director	SteerCo	H	M	Neutral	Supportive	Benefit credibility; baseline ownership	Eng Lead
S-08	Head of Business Direct	SteerCo; WG	M	H	Supportive	Champion	Volume handling; team capacity; pilot segment	BPR Lead
S-09	Head of Strategic Finance	SteerCo	M	M	Neutral	Supportive	RM time; customer experience for larger clients	BPR Lead
S-10	Head of Corporate	Consulted	M	L	Neutral	Neutral	Insider-information barriers respected	Eng Mgr
S-11	Head of MI & Regulatory Reporting	DA; data provider	M	M	Cautious	Supportive	Reporting fields protected; extract workload	Data/MI Analyst
S-12	Head of SBS/PS	WG Distressed	M	M	Neutral	Supportive	CAP journeys kept workable	Lending SME 1
S-13	Head of Lending Services	DA; WG	M	H	Supportive	Champion	Security process; manual hand-offs	Lending SME 2

ID	Stakeholder	Role in project	Influence	Interest	Current stance	Required stance	Key concern	Engagement owner
S-14	Head of Fulfilment	DA; WG	M	H	Supportive	Champion	Pre-conditions clarity; message quality from RMs	Lending SME 2
S-15	Senior RMs (×2)	DA; WG	M	H	Mixed	Supportive	Time spent on system vs customers; fear of headcount	BPR Lead
S-16	Business Direct Team Leaders	WG	L	H	Supportive	Champion	Renewal volume; fast-track	BPR Lead
S-17	Credit Managers	WG	M	H	Cautious	Supportive	Workload shift if fast-track removes low-risk cases; quality of submissions	Controls Specialist
S-18	RPA / Blue Prism team	Consulted	L	M	Neutral	Neutral	Bots retired without replacement	Platform Analyst
S-19	Internal Audit	Informed	M	L	Neutral	Neutral	Control changes evidenced	Controls Specialist
S-20	RM population (c. 600)	Survey; adopters	L	H	Unknown	Supportive	"What does this mean for me"	Change Lead
S-21	Experian (BLP vendor)	Informed	L	L	Neutral	Neutral	Quick-win changes on current BLP	Platform Analyst

2. Stakeholder map

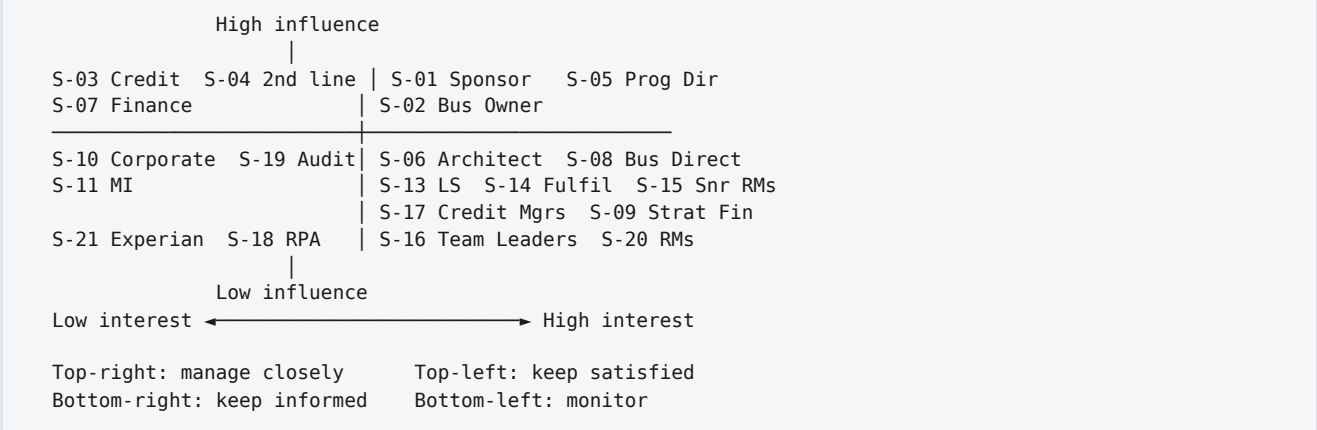

3. Engagement plan

Stakeholder group	Objective	Method	Frequency	Owner
Sponsor	Visible ownership; unblock	1:1	Weekly 30 min	Eng Lead
Business Owner	Day-to-day decisions; DA chair	1:1 + DA	Twice weekly	Eng Mgr
Credit Risk Policy, 2nd line	Move from cautious to supportive before Phase 2	Early 1:1s (W1–2); co-design of routing criteria; incremental control equivalence review	W1–2 then weekly from W8	Controls Specialist
Replacement Programme	Joint ownership of freeze date and requirements pack	Joint fortnightly; Programme Director on SteerCo; Architect on DA	Fortnightly	Eng Mgr, Platform Analyst
Finance	Own the baseline and benefits method	1:1 before G1 and G2; review of benefits logic tree	W2, W6, W11	Eng Lead

Stakeholder group	Objective	Method	Frequency	Owner
Front-line heads and team leaders	Release SMEs; champion fast-track	Working groups; 1:1 before G0 on SME hours	Weekly WG	BPR Lead
Credit Managers	Address workload-shift concern directly	WG Renewal; dedicated session on Credit workload under fast-track	W4, W9	Controls Specialist
Senior RMs	Workability; credibility with RM population	DA; walk-the-process; design reviews	Weekly Ph2	BPR Lead
RM population	Awareness; survey participation; later adoption	Sponsor message; team-leader cascades; survey; FAQ	W2, W5, W13, W17	Change Lead
MI & Reg Reporting	Timely extract; protected fields	1:1 W1; WG Controls & Data	Weekly	Data/MI Analyst
SBS/PS	Keep distressed journeys workable	WG Distressed	Fortnightly	Lending SME 1
Internal Audit	No surprises at control changes	Brief at G1 and G2	W7, W13	Controls Specialist
Corporate	Barriers respected	1:1 W1; proxies agreed	W1, W6	Eng Mgr

4. Key messages

From the Sponsor (kick-off and cascades)

- We are replacing BLP. This project makes sure we replace the process too, not just the screens.
- The focus is renewals and variations, two-thirds of what we do, where colleagues spend most time on steps that add no value to the customer or to credit quality.
- We will quantify capacity we can free up. What we do with it is a management decision after the design is approved, and it will be discussed openly.
- Credit control will not be weakened. Every control we change will be reviewed and signed off by Credit Risk and Risk.
- Your input in workshops and the one-week activity survey is how the new process gets designed around real work, not assumptions.

For Credit

- Fast-track is a routing decision you set the criteria for, with the data in front of you. It moves low-risk renewals out of your queue so you spend time on the cases that need judgement.

For the Replacement Programme

- You get a requirements pack in your backlog format by Week 13, with high-impact decisions released by Week 10.

5. Communications plan

ID	Communication	Audience	Purpose	Channel	Owner	Timing
C-01	Sponsor announcement	All Business Banking	Awareness; why; what to expect	Email + intranet	Sponsor (drafted by Change Lead)	W2
C-02	Kick-off	SteerCo, DA, WG leads, Programme	Launch; roles; plan	Meeting (0.10 deck)	Eng Lead	W2
C-03	Team-leader briefing pack	Team leaders	Cascade; SME release; survey	Pack + 30-min call	Change Lead	W2
C-04	Working-group launch	WG members	Purpose; schedule; how to prepare	Meeting	WG leads	W3
C-05	Activity survey launch	Sampled users	Participate; anonymised	Email from team leader; FAQ	Data/MI Analyst	W4 (Fri)

ID	Communication	Audience	Purpose	Channel	Owner	Timing
C-06	Weekly status report	Sponsor, Business Owner, Programme Director	Progress, RAG, decisions needed	Email, 1 page	PMO	Weekly Fri
C-07	SteerCo pack	SteerCo	Decisions	Pack	PMO	2 days before each SteerCo
C-08	G1 summary	All Business Banking leadership	Baseline findings	Intranet article + deck	Eng Mgr	W7
C-09	"What we heard" feedback	Workshop and interview participants	Close the loop	Email	BPR Lead	W7
C-10	Interim design release	Replacement Programme	Decisions so far	Document + session	Platform Analyst	W10
C-11	Design preview	Senior RMs, Credit Managers, Ops heads	Workability check before DA sign-off	Walkthrough	BPR Lead	W11
C-12	G2 announcement	All Business Banking	Approved design; what changes; next steps	Sponsor email + FAQ	Sponsor / Change Lead	W13
C-13	Pilot announcement	Pilot segment	What, when, support	Team meeting	Change Lead	W17

6. Feedback and measurement

- Workshop feedback form (3 questions) after each workshop; reviewed weekly
- Stakeholder stance re-assessed at each gate; register updated
- Survey response rate tracked daily in W5; escalate to team leaders below 60% by day 3

0.6 Hypothesis Tree and Discovery Mapping

Project	BB-BLP-BPR
Version	1.0 – for G0
Owner	WS1 Journeys & Process

1. Purpose

The hypothesis tree states what we believe is wrong and why, before discovery starts, so that Phase 1 collects evidence to prove or disprove specific claims rather than describing everything. Each leaf hypothesis has the evidence that would confirm it, the analysis that produces that evidence, the data source, the owner and the week.

Hypotheses are written to be falsifiable. "Renewals take too long" is not a hypothesis; "a material share of renewals could be decided within delegated authority without Credit review, with no increase in risk" is.

2. Governing question

Can Business Bank's lending lifecycle be redesigned so that time to decision and cost to serve fall materially, with credit control maintained, in a form the replacement platform can deliver as standard?

3. Tree

```
Governing question
│
├── A. Volume is concentrated in servicing journeys that are over-processed
│   ├── A1  Renewals follow the full credit flow despite no structural change
│   ├── A2  A material share of renewals meets objective low-risk criteria
│   ├── A3  EPR is used as a holding pattern, creating chains of extensions
│   └── A4  Variations are heterogeneous; a minority need full credit review
│
├── B. The journeys are structurally the same; the deal-type model multiplies them
│   ├── B1  Lead & Customer stage is identical across all journeys
│   ├── B2  Deal & Credit stage differs only by parameters, not by flow
│   ├── B3  Several deal types are redundant or non-customer (ESR Cleanse, DO NOT USE, Staged Drawdown orig.)
│   └── B4  Deal types carry their controls implicitly; controls can be made explicit as rules
│
├── C. Rework and wait, not touch time, dominate cycle time
│   ├── C1  "Deferred – further information required" is a high-frequency loop
│   ├── C2  Facility letter issue-and-return is the longest wait and a reset trigger
│   ├── C3  Changes after credit approval cause re-processing
│   └── C4  Hand-offs to Lending Services and Fulfilment carry queue time
│
├── D. Workarounds mask process and system gaps
│   ├── D1  Each bot and batch job substitutes for a missing process rule or system feature
│   ├── D2  Off-platform documents (Shadow Limit, Staged Drawdown letters) create control and data gaps
│   └── D3  Manual email issuance of letters creates audit and tracking gaps
│
├── E. Controls are a mix of policy, habit and system limitation
│   ├── E1  A share of control steps has no policy or regulatory source
│   ├── E2  Delegated-authority checks are performed manually where data exists to automate them
│   └── E3  Removing or automating controls is acceptable to second line if equivalence is shown
│
└── F. Data captured for reporting is at risk in any redesign unless mapped
    ├── F1  BLP fields feeding regulatory returns are not documented end to end
    └── F2  Operational MI relies on manual adjustment because capture is inconsistent
```

4. Hypothesis register

ID	Hypothesis	Evidence that would confirm	Analysis	Data source	Owner	Week	Links to
A1	Renewals follow the full Deal & Credit flow despite no structural change by definition	Stage sequence for Renewal matches New Money in ≥ 90% of cases	Stage-path analysis from BLP timestamps	MI extract DR-02	Data/MI Analyst	5	O1, O2
A2	≥ 40% of renewals meet objective low-risk criteria (limit unchanged, risk grade within band, covenants compliant, no watch-list, no EPR in 12 months)	Share of renewals meeting all criteria; historical default/downgrade rate of that population not worse than full-review population	Cohort analysis	DR-02, DR-05, DR-06	Controls Specialist, Data/MI Analyst	6	O1, O3; H3 in Approach
A3	EPR chains (2–3 consecutive) are common and precede a full renewal anyway	Share of EPRs followed by another EPR; share of chains reaching max 3	Sequence analysis	DR-02	Data/MI Analyst	5	O4
A4	≤ 30% of Variations change limit, security or pricing; the rest are administrative	Classification of variation reasons	Variation reason-code analysis; sample review of 50	DR-02, DR-04	Lending SME 2	5	O1, O5
B1	Lead & Customer stage steps are identical across all 7 mapped journeys	Deal type × stage matrix shows 100% common steps at stage 1	Matrix	Current maps; WS-02–10	BPR Lead	4	O5; H1
B2	Deal & Credit stage differs by parameters (which checks, which authority) not by flow	Matrix shows ≥ 80% common steps; differences expressible as rules	Matrix; rules extraction	WS-02–10; DR-07	BPR Lead, Controls Specialist	5	O5; H2
B3	ESR Cleanse, DO NOT USE and Staged Drawdown (origination) can be retired as deal types	ESR Cleanse has no credit decision; DO NOT USE has zero legitimate use; Staged Drawdown orig. = 0 in 12 months and is covered by Term Lending + allocation	Volume and purpose review	DR-01, DR-02	Lending SME 1	4	O5; H4, H5
B4	Type-specific controls (e.g. EPR max 3; Shadow Limit skips CDQ) can be stated as a rules table	All type-specific behaviours captured as rules with no residual flow difference	Rules extraction	WS-13; DR-07	Controls Specialist	6	O3, O5
C1	"Deferred – further information required" occurs on ≥ 20% of deals and adds ≥ 5 days	Loop frequency and added cycle time	Loop analysis	DR-02	Data/MI Analyst	5	O4
C2	Facility letter return is the longest single wait; ≥ 5% of letters hit the 3-month reset	Wait time distribution; reset count	Wait analysis	DR-02, DR-08	Data/MI Analyst	6	O4; H6
C3	Changes after credit approval occur on ≥ 10% of New Money/Increase deals	Re-processing count	Loop analysis; WS-11	DR-02	Lending SME 1	5	O4
C4	Queue time at Lending Services and Fulfilment exceeds touch time by ≥ 3×	Wait vs touch per hand-off	Timestamp + survey	DR-02, survey	Data/MI Analyst	6	O1

ID	Hypothesis	Evidence that would confirm	Analysis	Data source	Owner	Week	Links to
D1	Each of the 4 batch jobs and each bot covers a missing rule or feature that the to-be process should hold natively	Workaround inventory with root cause per item	Inventory	DR-09	Platform Analyst	5	O5; H7
D2	Off-platform letters for Shadow Limit and Staged Drawdown mean the platform does not hold the agreed terms	Confirmed by WS-09/10 and document review	Workshop; document sample	WS-09/10	Lending SME 2	5	O3, O6
D3	Manual email issuance of FALs has no systematic tracking of sent/returned status	Confirmed by walk-the-process; status captured only on return	Shadowing	Walk-the-process	Lending SME 1	4	O4, O6
E1	≥ 20% of control steps have no policy, regulatory or audit source	Control inventory source field = "practice"	Inventory	WS-13; DR-07	Controls Specialist	6	O2, O3
E2	Delegated-authority checks are manual although limit, grade and exposure data exist in BLP	Walk-the-process confirms manual check; BLP holds limit, grade and exposure fields	Shadowing; data availability check	Walk-the-process; DR-05	Controls Specialist	5	O1, O3
E3	Second line will accept automated or removed controls where equivalence is documented	Stated acceptance criteria obtained in W2 1:1	Interview	S-04	Controls Specialist	2	O3
F1	Regulatory returns sourced from BLP are not documented at field level	Lineage register gaps	Lineage mapping	DR-10	Data/MI Analyst	5	O6
F2	Operational MI requires manual adjustment because capture varies by segment	MI Manager interview; adjustment log	Interview; sample	S-11	Data/MI Analyst	4	O6

5. Exclusions and open questions

- We hold **no hypothesis on deposits** beyond location (SD-03); volume is too low to drive design.
- **Open:** whether the Replacement platform's standard process includes risk-based routing natively. Determines whether A2 becomes a configuration or a custom build. Resolved via D-07 by W8.
- **Open:** whether Corporate journeys differ structurally. Tested via proxy in WS-14.

6. How the tree is used

- Phase 1 workshops and analyses are planned against this register, not the other way round.
- Each hypothesis is marked Confirmed / Partly confirmed / Rejected in the current-state report (1.11) with the evidence.
- Rejected hypotheses are reported, not dropped; they are part of the fact base.
- The register is frozen at G0; new hypotheses raised in Phase 1 are added as "emergent" and reported separately.

0.7 Data Request and Data Provisioning Plan

Project	BB-BLP-BPR
Version	1.0 – issued Week 1 (Wed 11 Nov 2026)
Owner	WS3 Data & MI (Data/MI Analyst)
Bank owner	Head of MI & Regulatory Reporting

1. Purpose

This is the single data request for Phase 1. It is issued in Week 1 because MI lead time is 3–4 weeks and the baseline (G1, Week 7) depends on it. Items are prioritised: P1 is on the critical path; P2 improves the baseline; P3 is useful in Phase 2.

Period: **1 November 2025 – 31 October 2026** (12 months) unless stated.

2. Handling

- Customer-identifying fields pseudonymised at source (customer number → hash). Partner does not need names.
- Corporate segment records: supplied to Bank BA only; partner receives aggregates (SD-02).
- Delivery via Bank secure file transfer to the project SharePoint; no email.
- Data retained for the engagement only; deleted at closure.

3. Request

ID	Priority	Data item	Fields required	Grain	Source	Purpose / hypothesis	Due
DR-01	P1	Deal register	Deal ID, customer hash, segment, deal type, facility request type, created date, current status, closed date, officer code, created-by role, products on deal (type, limit, value), restructure flag	One row per deal	BLP	Volumes by type and segment; B3; baseline denominators	W4
DR-02	P1	Deal workflow stage history	Deal ID, stage/status code, stage entered timestamp, stage exited timestamp, actioned-by role, outcome code (approved / declined / deferred / withdrawn / referred)	One row per stage transition	BLP workflow tables	Cycle time per stage, loops, waits; A1, A3, C1–C4	W4
DR-03	P1	Decision outcomes	Deal ID, decision date, decision (approve / decline / defer / appeal), decision authority level, DCA/delegated-authority level used, within-authority flag	One row per decision	BLP	Delegated-authority analysis; E2	W4
DR-04	P2	Variation and EPR detail	Deal ID, variation reason code(s), fields changed (limit / pricing / security / covenant / dates / parties), EPR sequence number, prior EPR deal IDs	One row per deal	BLP	A3, A4	W5
DR-05	P1	Customer risk attributes at deal creation	Customer hash, risk grade, ECRS classification, lending category, watch-list flag, forbearance flag, total exposure, NAG exposure	Snapshot per deal	BLP / credit system	A2 fast-track cohort; E2	W5

ID	Priority	Data item	Fields required	Grain	Source	Purpose / hypothesis	Due
DR-06	P2	Post-decision performance	Customer hash, deal ID, subsequent risk-grade changes, arrears events, CAP referral within 12 months of decision	One row per event	BLP / credit system	A2 risk comparison of fast-track-eligible cohort	W6
DR-07	P1	Credit policy, delegated-authority matrix, procedure documents	Current versions; change log for 24 months	Documents	Credit Risk Policy	Control inventory; B4, E1	W3
DR-08	P1	Facility letter events	Deal ID, FAL generated date, sent date, sent method (post / secure email), returned date, checked date, 3-month reset flag	One row per letter	BLP (where captured) + RM mailbox proxy if not	C2, D3	W5
DR-09	P1	Automation inventory	Each Blue Prism bot and batch job: name, trigger, frequency, deal types affected, volumes processed in 12 months, failure/exception counts, business rule implemented, owner	One row per bot / job	RPA team; BLP support	D1; workaround inventory	W4
DR-10	P1	Regulatory and MI data lineage	For each regulatory return and standard MI report sourced from BLP: report name, frequency, BLP fields used, transformation, owner, manual adjustment steps	One row per report–field	MI & Reg Reporting	F1, F2; protected fields	W4
DR-11	P2	User and role register	User ID hash, role, segment, team, officer code, active flag, logins in period	One row per user	BLP admin	Survey sampling; effort baseline denominators	W3
DR-12	P2	Fulfilment and security hand-off events	Deal ID, "ready for fulfilment" timestamp, fulfilment complete timestamp, security instruction date, security complete date	One row per deal	BLP / Lending Services tracker	C4	W5
DR-13	P2	Deposit opportunities	Opportunity ID, created, status (won / declined by bank / declined by customer), value, product, RM	One row per opportunity	BLP	SD-03	W4
DR-14	P2	CAP referral and strategy events	Deal ID, referral date, SBS decision date, categorisation, strategy memo date, outcome	One row per event	BLP / SBS	Distressed journey baseline	W5
DR-15	P3	Existing MI reports and dashboards	Current operational MI packs (last 3 months)	Documents	MI	Baseline cross-check; F2	W4
DR-16	P3	Loaded cost rates by role	Fully loaded annual cost per role band (RM, Business Direct, Credit, Lending Services, Fulfilment, SBS)	Table	Finance	Cost per deal; business case	W6
DR-17	P3	Complaints and customer feedback relating to lending process	Count, theme, segment, period	Aggregated	Customer Experience	O7 baseline	W6
DR-18	P3	Replacement platform standard lending process documentation	Vendor process models, configuration options, standard workflow states	Documents	Replacement Programme / vendor	Fit-gap (Phase 2)	W8

4. Data quality checks on receipt

Check	Threshold	Action if failed
Deal count in DR-01 vs RFP figure (30,561)	± 5%	Reconcile with MI before use
Stage history completeness (DR-02): share of deals with full stage path	≥ 85%	Report baseline on complete subset; flag in G1
Timestamp sanity (exited ≥ entered; no future dates)	100% after cleansing	Exclude and report
Join rate DR-01 ↔ DR-02 ↔ DR-03	≥ 95%	Investigate key mismatch
FAL events (DR-08) coverage	Known; may be low	If < 50%, supplement with RM mailbox sampling in walk-the-process

5. Provisioning plan

Week	Action	Owner
1	Request issued; walkthrough with MI Manager (45 min); feasibility per item confirmed	Data/MI Analyst
1	Pseudonymisation and Corporate handling agreed with Information Security	Bank BA
2	DR-07, DR-11 received	Credit Risk Policy; BLP admin
3	Sample extract (1 month) of DR-01/02/03 for structure check	MI
4	DR-01, 02, 03, 09, 10, 13, 15 received	MI; RPA; Reg Reporting
5	DR-04, 05, 08, 12, 14 received	MI; Lending Services
6	DR-06, 16, 17 received	Credit; Finance; CX
8	DR-18 received	Replacement Programme

6. Activity survey (not an MI item; owned by WS3)

- Population: DR-11 users, sampled 15–20% stratified by role and segment (c. 150)
- Instrument: daily 15-minute self-report of time by activity category (c. 20 categories aligned to L2 taxonomy), Mon–Fri Week 5
- Anonymised; reported at role × segment level only
- Supplemented by time-and-motion on the five highest-volume activities (observed, not self-reported), Weeks 5–6

0.8 Replacement Programme Dependency Map and Joint Decision Log

Project	BB-BLP-BPR
Version	1.0 – agreed at joint session Week 1
Owner	WS4 (Platform/Integration Analyst) and Replacement Programme Manager

1. Why this document exists

The target-state design is only valuable if the Replacement Programme can still act on it. This document records the Programme's schedule constraints, what each party needs from the other and by when, and every joint decision. It is reviewed at the fortnightly joint session and its status is a standing SteerCo item.

2. Replacement Programme schedule constraints

Item	Date / status	Source	Impact on this project
Platform selection	**[Confirm W1]** – selected / shortlisted / not started	Programme Director	Determines whether Phase 2 fit-gap is against a product or a generic model (R-09)
Requirements baseline freeze	**[Confirm W1 in writing]**	Programme Director	Must be ≥ W13 (8 Feb 2027) for full design influence; interim release W10 mitigates (R-01)
Design / configuration start	[Confirm]	Programme PM	Requirements pack must precede this
Release 1 scope and date	[Confirm]	Programme PM	Determines which journey patterns are configured first; drives Phase 3 roadmap
Data migration design start	[Confirm]	Programme Data Lead	ESR Cleanse treatment (SD-01) must be communicated before this
Backlog tool and story format	[Confirm]	Programme BA Lead	Requirements pack (2.8) delivered in this format

3. Dependency map

3.1 What this project needs from the Programme

ID	Need	From	By	Status
P-01	Freeze date in writing	Programme Director	W1	Open
P-02	Editable current-state L3 maps	Programme PM	W1	Open
P-03	Platform standard lending process documentation (DR-18)	Programme / vendor	W8	Open
P-04	Solution Architect on Design Authority (3–6 hrs/week Ph2)	Programme Director	W2	Open
P-05	Backlog format and acceptance criteria for requirements	Programme BA Lead	W8	Open
P-06	Release plan (scope and dates)	Programme PM	W12	Open
P-07	Access to Programme requirements backlog (read)	Programme PM	W3	Open

3.2 What the Programme needs from this project

ID	Need	To	By	Status
B-01	ESR Cleanse treatment decision (SD-01)	Programme Data Lead	W2	Open
B-02	Deal types to retire / retain (B3)	Programme BA Lead	W7 (G1)	Open

ID	Need	To	By	Status
B-03	Journey patterns and design principles	Solution Architect	W8	Open
B-04	Interim design-decision release: patterns, routing concept, letter and e-signature approach, deal start component, retired workarounds	Programme	W10	Open
B-05	Fit / Configure / Custom / Gap classification per step	Solution Architect	W11	Open
B-06	Requirements pack: journey configuration, rules catalogue, epic-level stories, interface requirements, data requirements	Programme BA Lead	W13 (G2)	Open
B-07	Protected regulatory and MI fields list	Programme Data Lead	W7	Open
B-08	Quick-win list deliverable on current BLP (so Programme does not duplicate)	Programme PM	W13	Open
B-09	Design artefact handover (final maps, rules, TOM)	Programme BA and Test Leads	W17 (G3)	Open

4. Design decisions the Programme is waiting on

Ordered by the latest date each can change without affecting the Programme. This ordering drives the Phase 2 sequence.

ID	Decision	Programme impact if late	Latest date	Our planned date
DD-01	ESR Cleanse in or out of deal model	Migration design	W2	W2 (G0)
DD-02	Deal type model (which types exist)	Data model, workflow configuration	W8	W7
DD-03	Shared "deal start" component vs per-journey	Workflow configuration	W10	W8
DD-04	Risk-based routing: native capability vs custom	Build scope	W10	W10
DD-05	Facility letter generation and e-signature approach	Document and integration scope	W10	W10
DD-06	Deposit opportunity location (SD-03)	Opportunity object scope	W7	W7
DD-07	Which bots / batch jobs are retired vs rebuilt	Integration and automation scope	W11	W11
DD-08	Interface requirements: MEO, IMPACS, TELLER, CIF	Integration design	W13	W12
DD-09	Protected regulatory fields	Data model	W7	W7
DD-10	Corporate restricted-view requirements	Security model	W12	W12

5. Joint decision log

ID	Date	Decision required	Options	Decision	Rationale	Raised by	Owner	Status
JD-01	W1	Confirm freeze date and whether an interim release at W10 is usable by the Programme	(a) Freeze ≥ W13, interim at W10; (b) Freeze earlier, prioritised decisions only; (c) Freeze later	[Record at W1 session]		Eng Mgr	Programme Director	Open

ID	Date	Decision required	Options	Decision	Rationale	Raised by	Owner	Status
JD-02	W1	Maps ownership: who edits the L3 maps during Phase 1	(a) Project (Bank BA) edits, Programme reviews; (b) Programme edits on project instruction	Recommend (a)	Single owner during validation; handed back at G3	Platform Analyst	Programme PM	Open
JD-03	W2	ESR Cleanse treatment (SD-01)	See charter §5	[Record at G0]		Eng Mgr	SteerCo	Open
JD-04	W2	Requirements pack format	(a) Programme backlog tool, epic-level stories; (b) Document	Recommend (a)	Avoids re-keying; acceptance in-tool	Platform Analyst	Programme BA Lead	Open
JD-05	W3	Treatment of design decisions that arrive after freeze	(a) Change requests to Programme; (b) Phase 4 backlog	[Record]		Eng Mgr	Programme Director	Open

6. Joint session cadence

Fortnightly, 45 min, from Week 1: Engagement Manager, Platform/Integration Analyst, Programme PM, Solution Architect, Bank PM. Standing agenda: dependency status (§3), decisions due (§4), joint log (§5), risks shared with RAID (R-01, R-09, R-12).

7. Escalation

Unresolved dependency or decision after two joint sessions escalates to SteerCo, where the Programme Director and Sponsor both sit.

0.9 Benefits Logic Tree (Draft v0.1)

Project	BB-BLP-BPR
Version	0.1 – draft at G0; quantified at G1; owners named by W11
Owner	WS6 PMO & Benefits; reviewed with Finance Director W2

1. Purpose

The benefits logic tree shows the chain from design lever to measurable benefit before any number exists. It is agreed with Finance at G0 so that the method is not disputed at G2 when the numbers are. Every benefit in the business case must trace to a lever, a KPI, a baseline value and an owner.

2. Benefit categories

Category	Definition	How valued
Cash-releasing	Reduces cost that would otherwise be incurred	£ at loaded rate; only counted if a budget line changes
Capacity-releasing	Frees colleague time; treatment decided post-G2 (SD-04)	FTE-equivalent; £ shown at both redeployment value and cost-avoidance value
Risk and control	Reduces loss, exceptions or regulatory exposure	Qualitative, plus £ where loss data allows
Revenue-enabling	Faster decisions retain or win business	Qualitative at G2; quantified only with Finance agreement
Replacement cost avoidance	Reduces build, test and run cost of the replacement	£ from Programme estimates
Experience	Colleague and customer	Non-financial KPIs

3. Tree

```
Objective            Lever (design change)                              KPI
Benefit category
──────────           ─────────────────────                              ───
─────────────────
O1 Faster            L1  Risk-based fast-track for renewals             Renewal cycle time (P50, P80)
Capacity; Revenue-enabling
decisions            L2  Single deal-start component                    Lead-to-deal time; steps per journey
Capacity; Experience
                     L3  Automated delegated-authority check            Time in "validate / authority" stage
Capacity; Risk & control
                     L4  Automated letter generation and e-signature    FAL issue-to-return time
Capacity; Experience
                     L5  Exception paths designed (deferral, change     Time added by deferral loops
Capacity
                         after approval)

O2 Lower cost        L1, L2, L3, L4                                     Touch time per deal by type
Capacity (→ cash if SD-04 = a)
to serve             L6  Retire ESR Cleanse as a deal; retire dead      Deals processed; admin time
Capacity
                         deal types
                     L7  Retire bots / batch jobs replaced by native    RPA run and maintenance cost
Cash-releasing
                         rules
                     L8  Eliminate off-platform letters and manual      Lending Services / RM admin time
Capacity

O3 Credit control    L3  Automated delegated-authority check           Authority breaches; exceptions
Risk & control
maintained           L9  Controls made explicit as rules                Audit findings; control test results
Risk & control
```

```
                    L10 Native distress flags → CAP referral          Time from indicator to referral
Risk & control

04 Less rework      L4  Letter tracking, automated chase, expiry      3-month resets; unreturned letters
Capacity
                    L5  Exception-path design                         Deferral rate; re-processing rate
Capacity
                    L11 Submission quality rules at deal creation     First-time-right at Credit
Capacity (Credit)

05 Simpler          L12 11 deal types → 5 journey patterns            Deal types; workflow variants
Replacement cost avoidance
replacement         L13 Fit-to-standard; custom list minimised        Custom items; build and test effort
Replacement cost avoidance
                    L7, L8                                            Integrations retired
Replacement cost avoidance

06 Data             L14 Capture once at source; protected fields      Manual MI adjustments; DQ score
Risk & control; Capacity (MI)
                    L15 On-platform letters and terms                 Terms held on platform (%)
Risk & control

07 Experience       L2, L4, L5                                        RM steps per journey; RM survey;
Experience
                                                                      customer effort / NPS
```

4. Benefit register (skeleton, to be populated at G1)

ID	Benefit	Lever(s)	KPI	Baseline (G1)	Target (G2)	Category	Owner (by W11)	Realisation start	Measurement source
BN-01	Renewal cycle time reduction	L1, L2, L3	Renewal P80 cycle time			Capacity; Revenue	Head of Business Direct	Release 1	DR-02 equivalent on new platform
BN-02	Credit capacity released from low-risk renewals	L1	Credit touch time on renewals			Capacity	Head of Credit	Release 1	Activity survey re-run
BN-03	RM capacity released across servicing	L2, L4, L5, L6, L8	RM touch time per servicing deal			Capacity	Heads of segment	Release 1–2	Activity survey re-run
BN-04	Lending Services and Fulfilment capacity	L4, L8, L15	Touch time per deal			Capacity	Heads of LS, Fulfilment	Release 1	Activity survey re-run
BN-05	RPA run and maintenance cost avoided	L7	Bots retired; cost			Cash	Head of Technology Ops	Release 1–2	Technology cost centre
BN-06	3-month letter resets eliminated	L4	Reset count			Capacity	Head of Lending Ops	Release 1	Platform events
BN-07	Deferral loop reduction	L5, L11	Deferral rate; days added			Capacity	Head of Credit	Release 1	Platform events
BN-08	Replacement build and test effort avoided	L12, L13	Custom items; variants			Replacement cost avoidance	Programme Director	Design	Programme estimate
BN-09	Manual MI adjustment eliminated	L14	Adjustment hours / month			Capacity (MI)	Head of MI	Release 1	MI team log

ID	Benefit	Lever(s)	KPI	Baseline (G1)	Target (G2)	Category	Owner (by W11)	Realisation start	Measurement source
BN-10	Authority breach and exception reduction	L3, L9	Breaches; exceptions			Risk & control	Head of Credit Risk Policy	Release 1	Credit MI
BN-11	Earlier distress referral	L10	Indicator-to-referral days			Risk & control	Head of SBS	Release 2	SBS MI
BN-12	Colleague experience	L2, L4, L5	RM steps per journey; RM survey			Experience	Head of Lending Ops	Release 1	Survey

5. Counting rules (agreed with Finance)

1. Capacity is counted once, at the role where it is released, net of any new activity the design adds to that role.
2. Capacity converts to cash only if SD-04 is decided as (a) and a budget line changes; otherwise reported as FTE-equivalent with a redeployment value.
3. Replacement cost avoidance uses the Programme's own estimates; this project does not estimate build cost.
4. Revenue-enabling benefits are described at G2 and quantified only if Finance agrees a method.
5. Baselines are frozen at G1 and re-measured at the same grain after each release.
6. Dis-benefits (e.g. Credit workload concentration on complex cases, training time) are recorded alongside benefits.

6. Dis-benefit register (skeleton)

ID	Dis-benefit	Cause	Affected	Mitigation
DB-01	Credit caseload becomes more complex on average	Fast-track removes simple cases	Credit Managers	Role profile and resourcing reviewed in TOM
DB-02	Training and transition time	New journeys and platform	All roles	Counted as one-off cost in business case
DB-03	Temporary productivity dip at go-live	Change	All roles	Hypercare; phased rollout

0.10 Kick-off Deck

Business Lending Process Redesign ahead of the BLP Replacement Kick-off · Week 2 · Thursday 19 November 2026 · 90 minutes Audience: SteerCo, Design Authority, Working-group leads, Replacement Programme leadership

Slide content below; one block per slide. Speaker notes in italics.

Slide 1 – Title

Business Lending Process Redesign ahead of the BLP Replacement Kick-off · 19 November 2026 Presented by: Executive Sponsor; Engagement Lead

---

Slide 2 – Why we are here (Sponsor)

- BLP is being replaced. If we replace the screens but keep the process, we carry 11 deal types, four batch jobs, a set of bots and manual facility letters onto a new platform.
- 30,561 deals last year. Two-thirds were renewals and variations, where colleagues spend most time on steps that add nothing to the customer or to credit quality.
- This project designs the process the new platform will be built to. It runs 17 weeks to ready-to-implement, with the design and business case approved in 13.
- Three commitments: credit control is not weakened; capacity we free is a management decision made openly after the design; your time in workshops is how the design gets built around real work.

Sponsor delivers this slide in their own words. Message 3 addresses the headcount concern directly (R-05).

Slide 3 – What the numbers tell us already

Deals, 12 months	30,561
Renewal + Variation	66%
New Money	2.3%
ESR Cleanse (records transfer, not a deal)	12.5%
Staged Drawdown originations	0
Deal types	11, of which 1 is "DO NOT USE"
Users	c. 900
Facility letters	Manual PDF by email; 3-month unreturned reset
Workarounds	Blue Prism bots; 4 batch jobs; off-platform letters

We have not baselined anything yet. These are the facts from the RFP and the maps; Phase 1 puts time and cost against them.

Slide 4 – Objectives

#	Objective	We will know at G2 because…
O1	Faster decisions, priority on servicing	Cycle-time targets per pattern set against the baseline
O2	Lower cost to serve, capacity released	Capacity by role quantified with named owners
O3	Credit control maintained or strengthened	Every control change has signed equivalence
O4	Less rework	Loops quantified and designed out
O5	Simpler for the replacement	11 types → c. 5 patterns; requirements pack in the Programme backlog
O6	Regulatory and MI data protected	Lineage documented; no field removed without sign-off
O7	Better colleague and customer experience	Steps per journey reduced; measure agreed

Slide 5 – Scope on one page

In: all lending journeys on BLP (origination, decision, documentation, servicing, distressed, pre-approved drawdown); deposits recording; 12 products; 11 deal types; all segments; embedded controls; bots, batch jobs, off-platform documents. **Out:** Personal Association Lend; platform selection and build; credit policy content; other systems beyond interfaces. **Decided today (G0):** ESR Cleanse → specify for migration, then out · Corporate → via proxies · Deposits location → decide by G1 · Capacity → quantify; treatment post-G2.

Slide 6 – Approach: five phases, four gates

```
Mobilise → Discover → Design → Plan delivery → Implement & track
 W1–2       W3–7       W8–13     W14–17          W18+
  G0         G1         G2         G3
Charter    Baseline   Design +   Ready to
approved   endorsed   business   implement
                      case;
                      funding
```

Six workstreams: Journeys & Process · Controls · Data & MI · Technology & Replacement interface · People & Change · PMO & Benefits.

Slide 7 – What makes this different from a generic process review

1. **Servicing first.** Design effort goes where the volume is.
2. **Fit-to-standard.** Adopt the platform's standard journey where good enough; custom only with a documented reason.
3. **Control equivalence.** No control removed or automated without a signed replacement. Second line is on the Design Authority from day one, not at the end.
4. **Route by risk, not by deal type.** Fast-track criteria co-designed with Credit Risk using our own data.
5. **A deliverable the Programme can build.** Requirements pack in the backlog by Week 13; high-impact decisions released Week 10.

Slide 8 – Our starting hypotheses (to be tested, not assumed)

- A material share of renewals could be decided within delegated authority without full Credit review, with no increase in risk
- The seven mapped journeys share one Lead & Customer stage and a near-identical Deal & Credit flow; deal types differ by parameters, not by process
- Rework and wait, not touch time, dominate cycle time: deferrals, letter return, changes after approval
- Each bot and batch job covers a missing rule the new process should hold natively
- A share of control steps has no policy source

Full tree in 0.6. We will report each as confirmed, partly confirmed or rejected at G1.

Slide 9 – Governance

```
Sponsor → SteerCo (fortnightly; gates, scope, funding)
            ├─ Design Authority (weekly Ph2; design and control sign-off)
            │     incl. Credit Risk Policy · 2nd-line Risk · MI/Reg Reporting · Solution Architect
            ├─ Project leadership (Eng Mgr + Bank PM, daily)
            └─ Replacement Programme joint session (fortnightly; freeze date, decision log)
Working groups: New/Increase · Servicing · Renewal & EPR · Distressed · Pre-approved Drawdown · Controls &
Data
```

Escalation: WG → Eng Mgr/Bank PM (2 days) → DA → SteerCo → Sponsor.

Slide 10 – Plan and milestones

Week	Milestone
1	Data request issued; Replacement dependency agreed
2	**G0** today
3	Working groups launch; 14 validation workshops W3–6
5	Activity survey (one week, c. 150 colleagues, 15 min/day)
7	**G1** baseline endorsed
8	Design principles and journey patterns
10	Interim design release to Replacement Programme
12	Design Authority sign-off
13	**G2** design and business case; requirements pack handed over
17	**G3** ready to implement

Slide 11 – The Replacement Programme dependency

- Freeze date: **[confirmed / to confirm]**
- We release high-impact decisions at W10: deal-type model, deal-start component, routing approach, letter and e-signature approach, retired workarounds
- Full requirements pack in the Programme backlog format at W13
- Programme Director on SteerCo; Solution Architect on Design Authority; joint session fortnightly

If the freeze date is earlier than W13, say so now; the plan re-sequences around it (R-01).

Slide 12 – What we need from you

Who	What	When
Heads of function	Release named SMEs (hours in plan)	Confirm today
Credit Risk Policy, 2nd line	1:1 this week; join Design Authority	W2
MI & Reg Reporting	Data request walkthrough; extract by W5	W1–5
Replacement Programme	Freeze date in writing; editable maps; Architect time	W1–2
Team leaders	Cascade briefing; survey sponsorship	W2, W4
Everyone	Parking lot discipline: platform build and policy content are out of scope	Ongoing

Slide 13 – Top risks

Risk	What we are doing
Programme freezes before our design lands	Freeze date in writing; interim release W10
MI extract late	Request issued W1; survey and time-and-motion run independently
Late control objections	2nd line on DA from W2; incremental review
SME availability	Hours agreed today; off month-end
Seen as a headcount exercise	Sponsor message; capacity treatment decided post-G2

Slide 14 – Decisions required today (G0)

1. Approve the charter, including scope decisions SD-01 to SD-04
2. Approve governance: SteerCo and Design Authority membership and cadence
3. Approve the integrated plan and Bank resource commitment
4. Confirm the Replacement Programme freeze date
5. Confirm SteerCo availability for G1 (Week 7, pre-Christmas) or move to Week 8

Slide 15 – Next two weeks

- W2: 1:1s with Credit Risk Policy and 2nd line; team-leader briefing; Sponsor announcement
- W3: working groups launch; taxonomy workshop; first journey validation workshops; survey design
- W3: MI sample extract for structure check
- Weekly status every Friday to Sponsor, Business Owner, Programme Director

Appendix

- A1 Deal types and 12-month volumes (from RFP)
- A2 Workshop schedule W3–6 (from 0.3 §6)
- A3 Data request summary (from 0.7)
- A4 Stakeholder engagement plan (from 0.5)
