BUSINESS BANK · BUSINESS BANKING TRANSFORMATION OFFICE · BB-BLP-BPR


2.3 To-Be Process Maps L3/L4

Shared components, patterns and exception paths, with every as-is step dispositioned

Deliverable	2.3 To-be process maps per pattern and shared component; disposition of every as-is step
Version	0.6 – design draft for working-group review (Weeks 9–10) and RM / Credit preview (Week 11); v1.0 at Design Authority sign-off (Week 12)
Derived from	2.1 principles; 2.2 pattern definitions; 1.2 as-is maps (same notation); 1.3 step matrix (disposition rows); 1.6 controls; 1.10 opportunities
Owner	WS1 Journeys & Process
Accepted by	Design Authority; subject to 2.5 equivalence entries CE-001, CE-002 and policy questions PQ-001, PQ-002

How to read this document

Legend



Structure

Section 1 maps the three shared components (SC-1a, SC-1b, SC-2, SC-3), which carry most of the design. Section 2 maps the pattern-specific segments (P3 removal, P5) and the four exception paths that are now first-class. Section 3 shows each pattern as a composition. Section 4 is the disposition register: every one of the 62 as-is step rows from 1.3, marked Eliminated, Automated, Consolidated or Retained, with the to-be location, the reason, the principle applied and the control effect. Section 5 lists the design decision records and the equivalence and policy items the maps depend on.

Conventions

Same notation as 1.2. Grey boxes are platform (automated) steps; Cn badges are controls from 1.6, retained or relocated; new controls are named in notes. Where a step is labelled with an RS-nn reference, its behaviour is set by that rules table in 2.4 rather than by the map.

What changes, in numbers


Disposition	As-is step rows	Meaning
Eliminated	5	Work stops; the need is removed by design
Automated	32	The platform performs it, with evidence
Consolidated	2	Merged with another step or relocated
Retained	23	Still a human step, usually with a rule or evidence added

Of the 62 rows, 37 (60%) are eliminated or automated. No regulatory control is eliminated; four controls are relocated or converted to reconciliations; nine are strengthened.

1. Shared components

TB-SC1a · SC-1 Deal start · existing relationship

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-05, DP-08, DP-09	RN-1, VA-1, RF-1, CR-1, CS-1, SR-1 (start), SD-1 (start); NM-1 for Increase	OP-10, OP-14, OP-22	Customer · RM · Platform

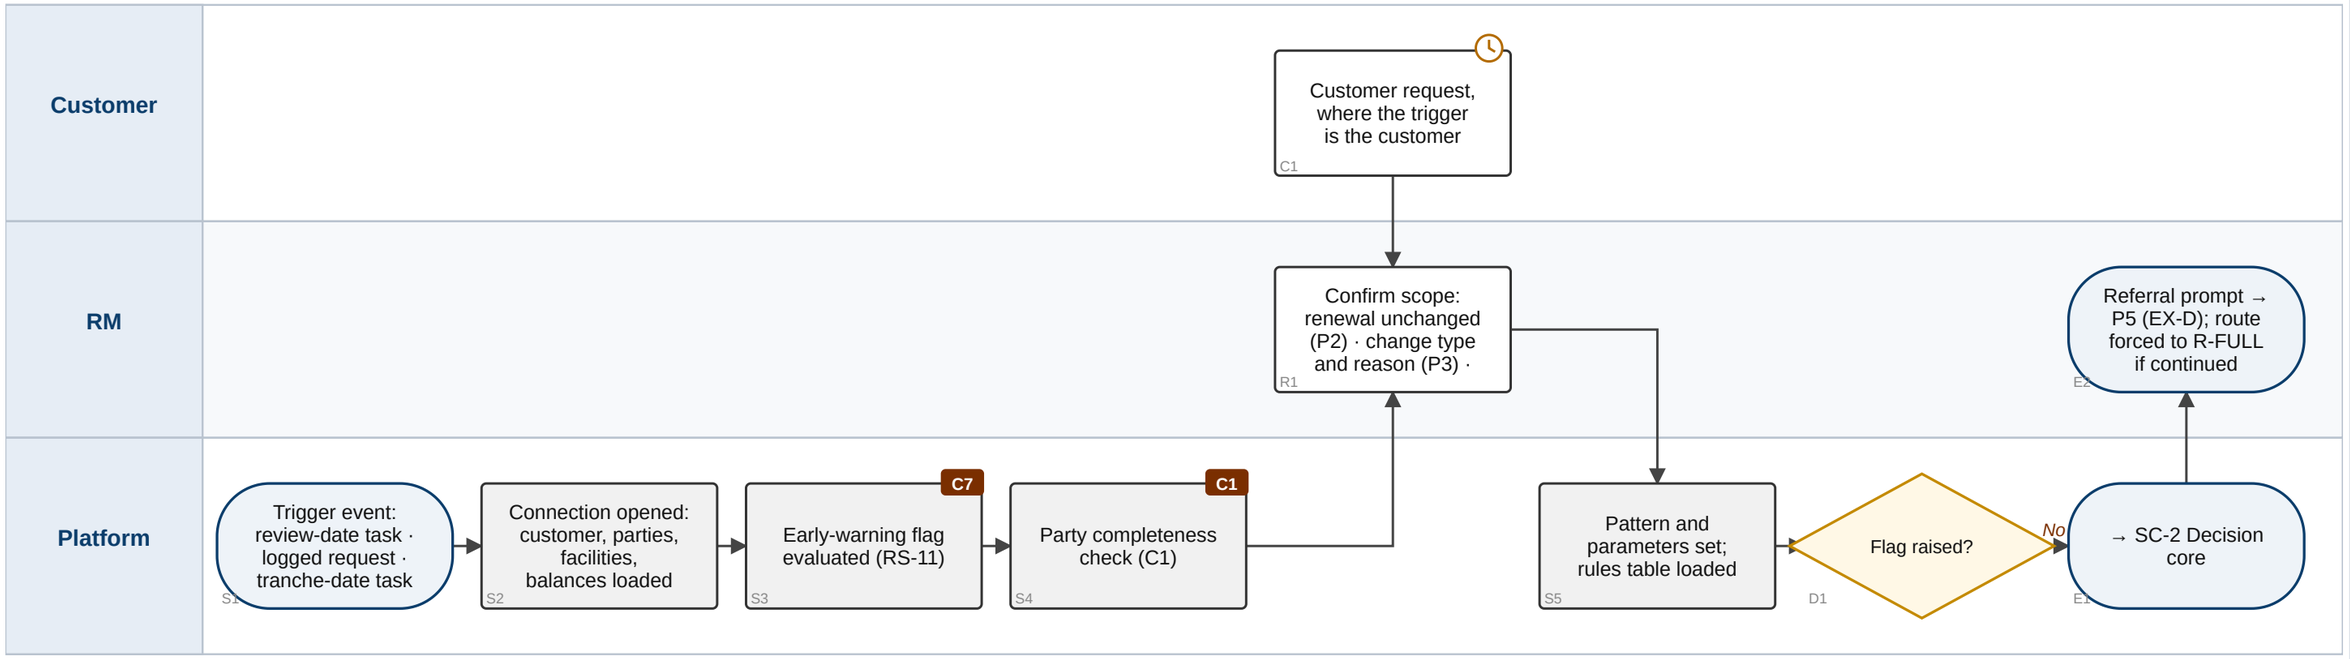

Design notes


- Five manual as-is steps become one automated step (S2). The RM's first action is to confirm scope, not to find the customer.
- The early-warning evaluation at S3 is the exclusion gate for every fast-track route and the trigger for P5.
- Opportunity record retired as an object; "opportunity" is a deal status.

L4 step table

ID	Lane	Step	Type	Control	Wait	Note / rule reference
S1	Platform	Trigger event: review-date task · logged request · tranche-date task · early-warning flag	Start			New: system event replaces report / email / phone (RS-11 for flags)
S2	Platform	Connection opened: customer, parties, facilities, balances loaded	Platform			Automated: replaces login, landing, search, locate, retrieve (PP-03); balances via integration (OP-32)
S3	Platform	Early-warning flag evaluated (RS-11)	Platform	C7		C7 relocated from end of Credit assessment to deal start
S4	Platform	Party completeness check (C1)	Platform	C1		New rule: partnerships / Ltd parties present
R1	RM	Confirm scope: renewal unchanged (P2) · change type and reason (P3) · allocation (P4)	Manual			Reason code captured (RS-03)
C1	Customer	Customer request, where the trigger is the customer	Manual		●	Digital intake or RM-logged; structured
S5	Platform	Pattern and parameters set; rules table loaded	Platform			Deal type, product, segment, risk band
D1	Platform	Flag raised?	Decision			
E2	RM	Referral prompt → P5 (EX-D); route forced to R-FULL if continued	End			
E1	Platform	→ SC-2 Decision core	End			

TB-SC1b · SC-1 Deal start · new customer

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-02, DP-05, DP-09	NM-1, SL-1 (new-customer path)	OP-08, OP-14, OP-29	Customer · RM · Platform

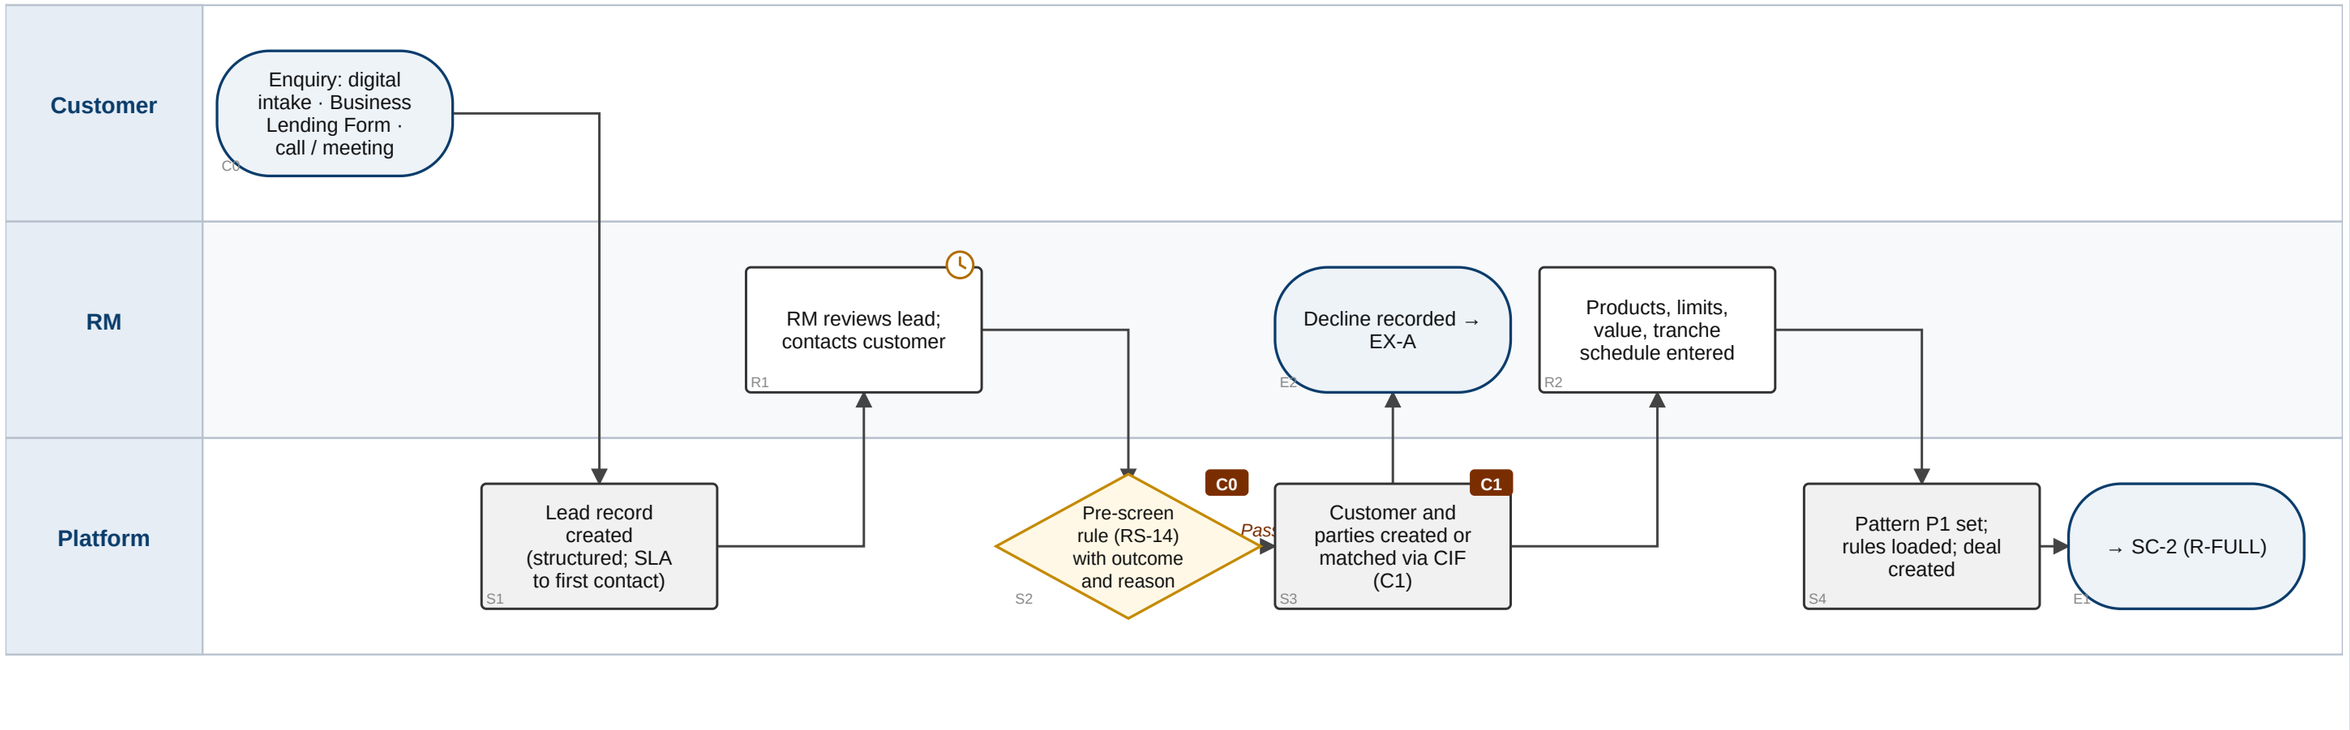

Design notes


- Lead becomes a record with an SLA; the enquiry-to-contact gap (PP-01) is measured for the first time.
- Pre-screen declines are recorded with a reason code, closing the conduct gap (RR-07).
- Tranche schedule captured here is consumed by P4; the Staged Drawdown origination type is retired.

L4 step table

ID	Lane	Step	Type	Control	Wait	Note / rule reference
C0	Customer	Enquiry: digital intake · Business Lending Form · call / meeting	Start			
S1	Platform	Lead record created (structured; SLA to first contact)	Platform			New: lead register (PP-01)
R1	RM	RM reviews lead; contacts customer	Manual		●	
S2	Platform	Pre-screen rule (RS-14) with outcome and reason code	Decision	C0		C0 becomes a rule with recorded outcome (PP-02)
E2	RM	Decline recorded → EX-A	End			
S3	Platform	Customer and parties created or matched via CIF (C1)	Platform	C1		
R2	RM	Products, limits, value, tranche schedule entered	Manual			
S4	Platform	Pattern P1 set; rules loaded; deal created	Platform			
E1	Platform	→ SC-2 (R-FULL)	End			

TB-SC2 · SC-2 Decision core · routes R-FULL, R-FAST, R-EXC

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-01, DP-02, DP-03, DP-04, DP-07	NM-2, RN-2, VA-2, SL-2, SR-1 / SD-1 (decision stages)	OP-01, OP-02, OP-05, OP-06, OP-07, OP-17, OP-18	Customer · RM · Platform · Credit

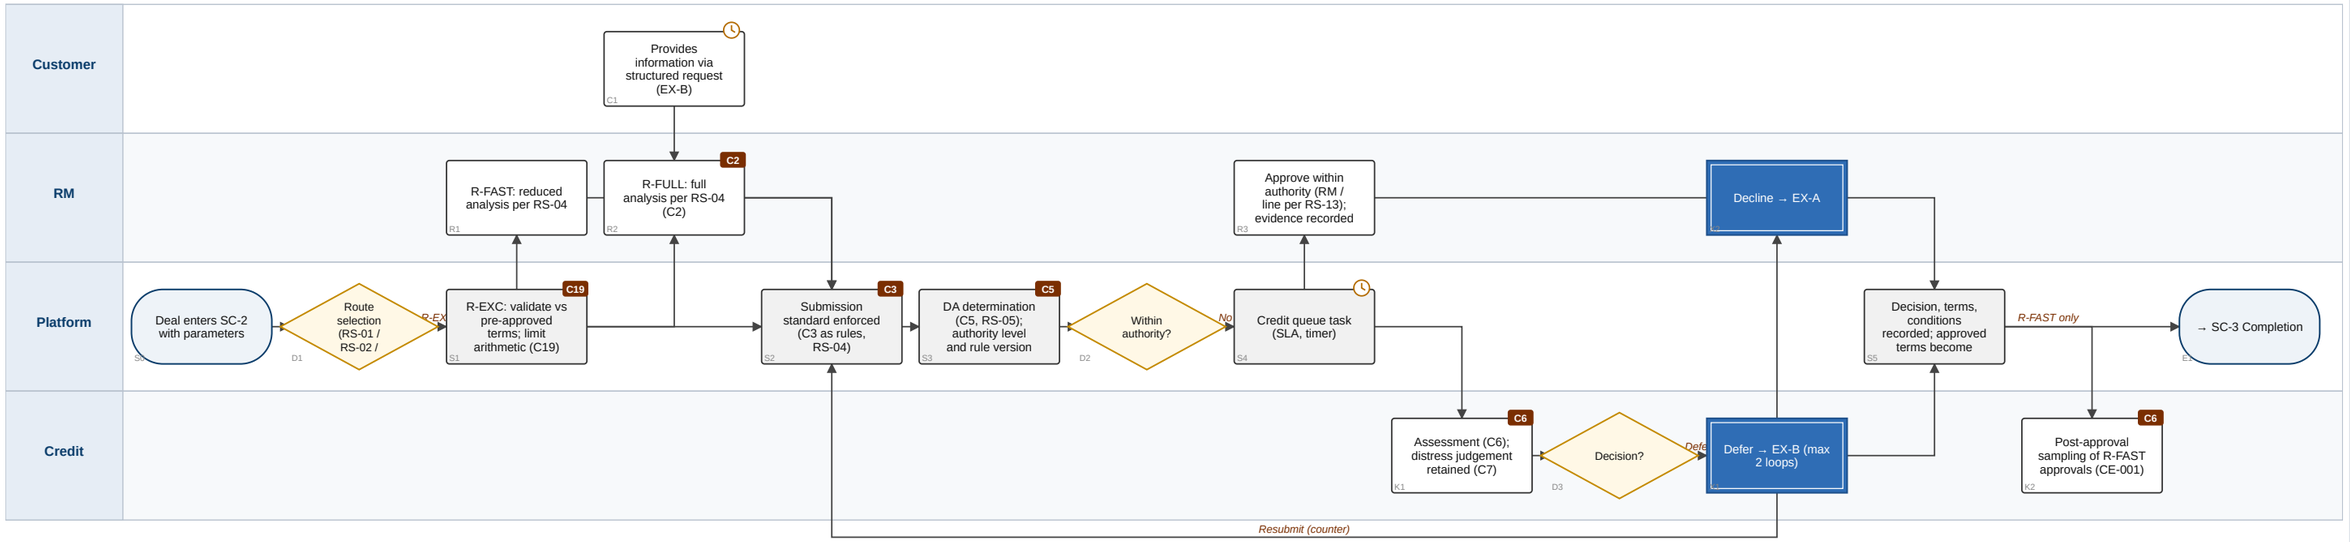

Design notes


- One configured flow; three routes selected by rules on system-held data. Deal type is a column in RS-01 to RS-05, not a workflow.
- The deferral loop is bounded (RS-09) and the submission standard (S2) is intended to make it the exception.
- R-FAST bypasses K1 for eligible deals; equivalence is the automated DA determination with recorded evidence plus Credit sampling (CE-001). Activation depends on G1 decision 2.
- The “Progress?” judgement on the as-is maps becomes a recorded decision with reason (withdraw / decline / proceed).

L4 step table

ID	Lane	Step	Type	Control	Wait	Note / rule reference
S0	Platform	Deal enters SC-2 with parameters	Start			
D1	Platform	Route selection (RS-01 / RS-02 / RS-03)	Decision			Flag raised → R-FULL forced
R1	RM	R-FAST: reduced analysis per RS-04	Manual			Eligibility evidence attached automatically
R2	RM	R-FULL: full analysis per RS-04 (C2)	Manual	C2		Analytics on platform or integrated (OP-19)
S1	Platform	R-EXC: validate vs pre-approved terms; limit arithmetic (C19)	Platform	C19		Automated: Σ allocations ≤ limit
C1	Customer	Provides information via structured request (EX-B)	Manual		●	
S2	Platform	Submission standard enforced (C3 as rules, RS-04)	Platform	C3		Cannot submit until items present (OP-17)
S3	Platform	DA determination (C5, RS-05); authority level and rule version recorded	Platform	C5		Automated (OP-06); manual override with reason
D2	Platform	Within authority?	Decision			
R3	RM	Approve within authority (RM / line per RS-13); evidence recorded	Manual			
S4	Platform	Credit queue task (SLA, timer)	Platform		●	Queue visible to RM (OP-11)
K1	Credit	Assessment (C6); distress judgement retained (C7)	Manual	C6		
D3	Credit	Decision?	Decision			
X1	Credit	Defer → EX-B (max 2 loops)	Sub-process			
X2	RM	Decline → EX-A	Sub-process			
S5	Platform	Decision, terms, conditions recorded; approved terms become document source	Platform			
K2	Credit	Post-approval sampling of R-FAST approvals (CE-001)	Manual	C6		New compensating control
E1	Platform	→ SC-3 Completion	End			

TB-SC3 · SC-3 Completion · gates G-DOC, G-SEC, G-CP

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-04, DP-06, DP-07, DP-09	NM-3, VA-3, SL-3, SR-2, SD-2, RN-3; EX-05	OP-13, OP-15, OP-16, OP-21	Customer · RM · Platform · Lending Services · Fulfilment

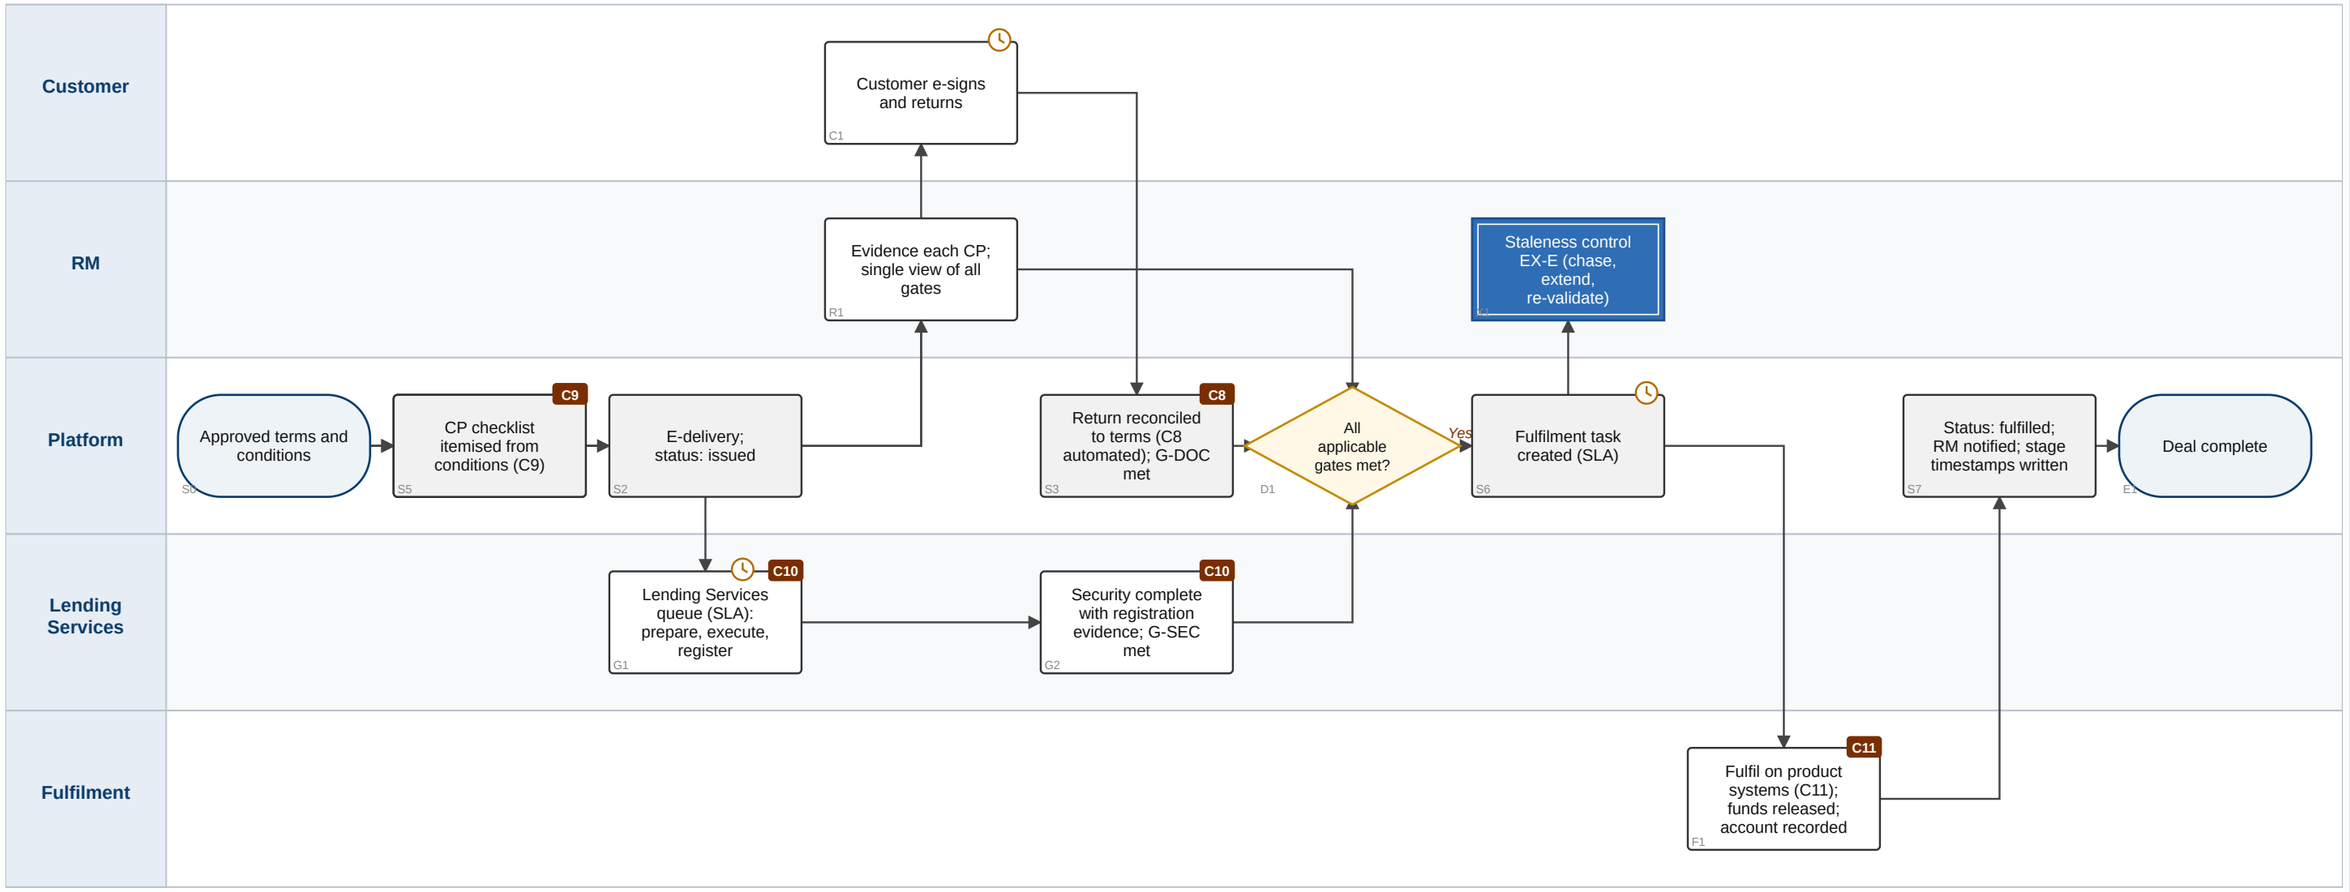

Design notes

- Three gates run in parallel from the approved terms; the single view (R1) replaces three disconnected flags.
- The letter is a system object with status; issue, return and reconciliation are facts, not mailbox searches. C4 (document check) becomes the reconciliation at S3.
- Variants: Short (P2: G-DOC only, letter per rule), Gated (P3: G-SEC only if security changes; fulfilment only if facility changes), Light (P4), Full (P1).
- Removal variant (P3) is mapped separately (TB-P3R).

L4 step table


ID	Lane	Step	Type	Control	Wait	Note / rule reference
S0	Platform	Approved terms and conditions	Start			
S1	Platform	Letter generated from terms (RS-06); letter-required rule applied	Platform			Templates per pattern and product incl. tranches, shadow limits
S2	Platform	E-delivery; status: issued	Platform			Wet-ink exception path (DB-05)
C1	Customer	Customer e-signs and returns	Manual		●	Chase timers EX-E (RS-08)
S3	Platform	Return reconciled to terms (C8 automated); G-DOC met	Platform	C8		
S4	Platform	Security instruction generated from conditions (C23); LS task	Platform	C23		Only when RS-07 says security changes

G1	Lending Services	Lending Services queue (SLA): prepare, execute, register	Manual	C10	●	
G2	Lending Services	Security complete with registration evidence; G-SEC met	Manual	C10		
S5	Platform	CP checklist itemised from conditions (C9)	Platform	C9		
R1	RM	Evidence each CP; single view of all gates	Manual			OP-13
D1	Platform	All applicable gates met?	Decision			
X1	RM	Staleness control EX-E (chase, extend, re-validate)	Sub-process			Replaces 3-month reset (CE-002)
S6	Platform	Fulfilment task created (SLA)	Platform		●	Replaces message (PP-29)
F1	Fulfilment	Fulfil on product systems (C11); funds released; account recorded	Manual	C11		
S7	Platform	Status: fulfilled; RM notified; stage timestamps written	Platform			
E1	Platform	Deal complete	End			

2. Pattern-specific segments and exception paths

TB-P3R · P3 Servicing change · removal variant

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-03, DP-04, DP-09	RF-2	OP-02, OP-26	RM · Platform · Securities Team · Fulfilment

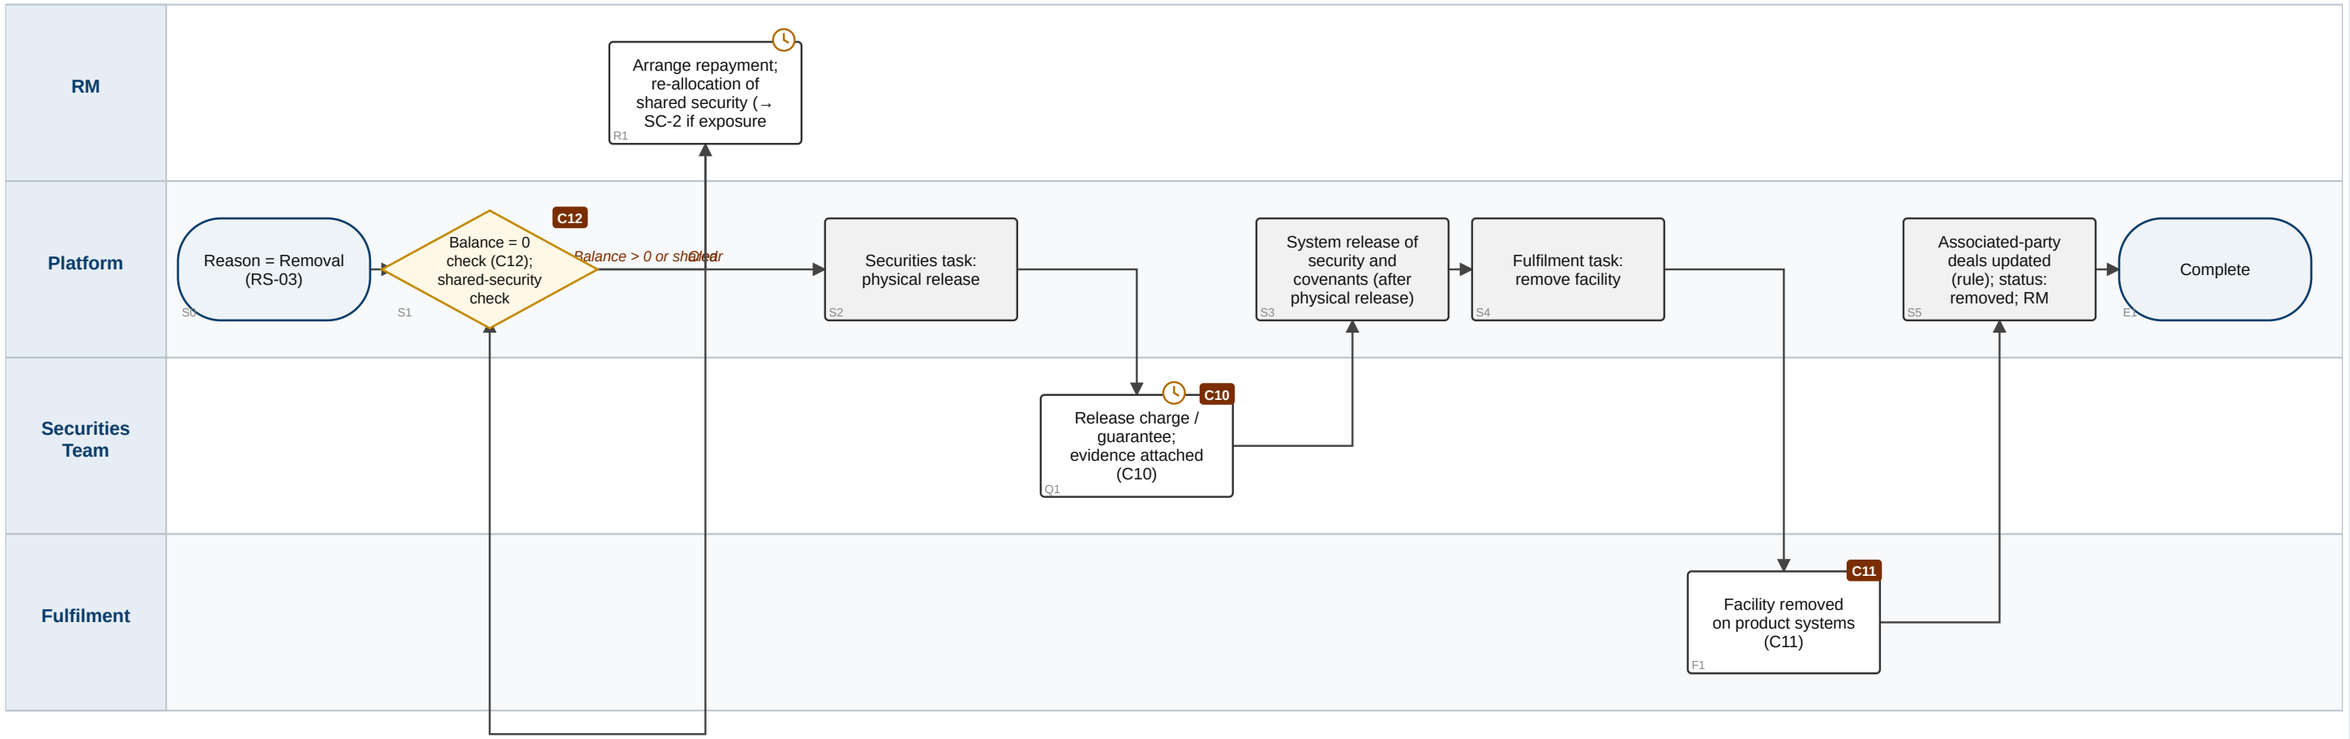

Design notes


- Four messages become two tasks with SLAs.
- Physical release precedes system release; the as-is order is reversed.
- Shared security is checked by rule before release, closing the exposure gap noted on RF-2.

L4 step table

ID	Lane	Step	Type	Control	Wait	Note / rule reference
S0	Platform	Reason = Removal (RS-03)	Start			
S1	Platform	Balance = 0 check (C12); shared-security check	Decision	C12		System checks balance; identifies security shared with other facilities
R1	RM	Arrange repayment; re-allocation of shared security (→ SC-2 if exposure elsewhere depends on it)	Manual		●	
S2	Platform	Securities task: physical release	Platform			
Q1	Securities Team	Release charge / guarantee; evidence attached (C10)	Manual	C10	●	
S3	Platform	System release of security and covenants (after physical release)	Platform			Sequence corrected (PP-30)
S4	Platform	Fulfilment task: remove facility	Platform			
F1	Fulfilment	Facility removed on product systems (C11)	Manual	C11		
S5	Platform	Associated-party deals updated (rule); status: removed; RM notified	Platform			Resolves RF-2 TBC
E1	Platform	Complete	End			

TB-P5 · P5 Distressed connection

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-08, DP-09, DP-02	CR-1, CR-2, CS-1, CS-2, EX-04	OP-20, OP-22, OP-23, OP-26	RM · Platform · Credit · SBS / PS

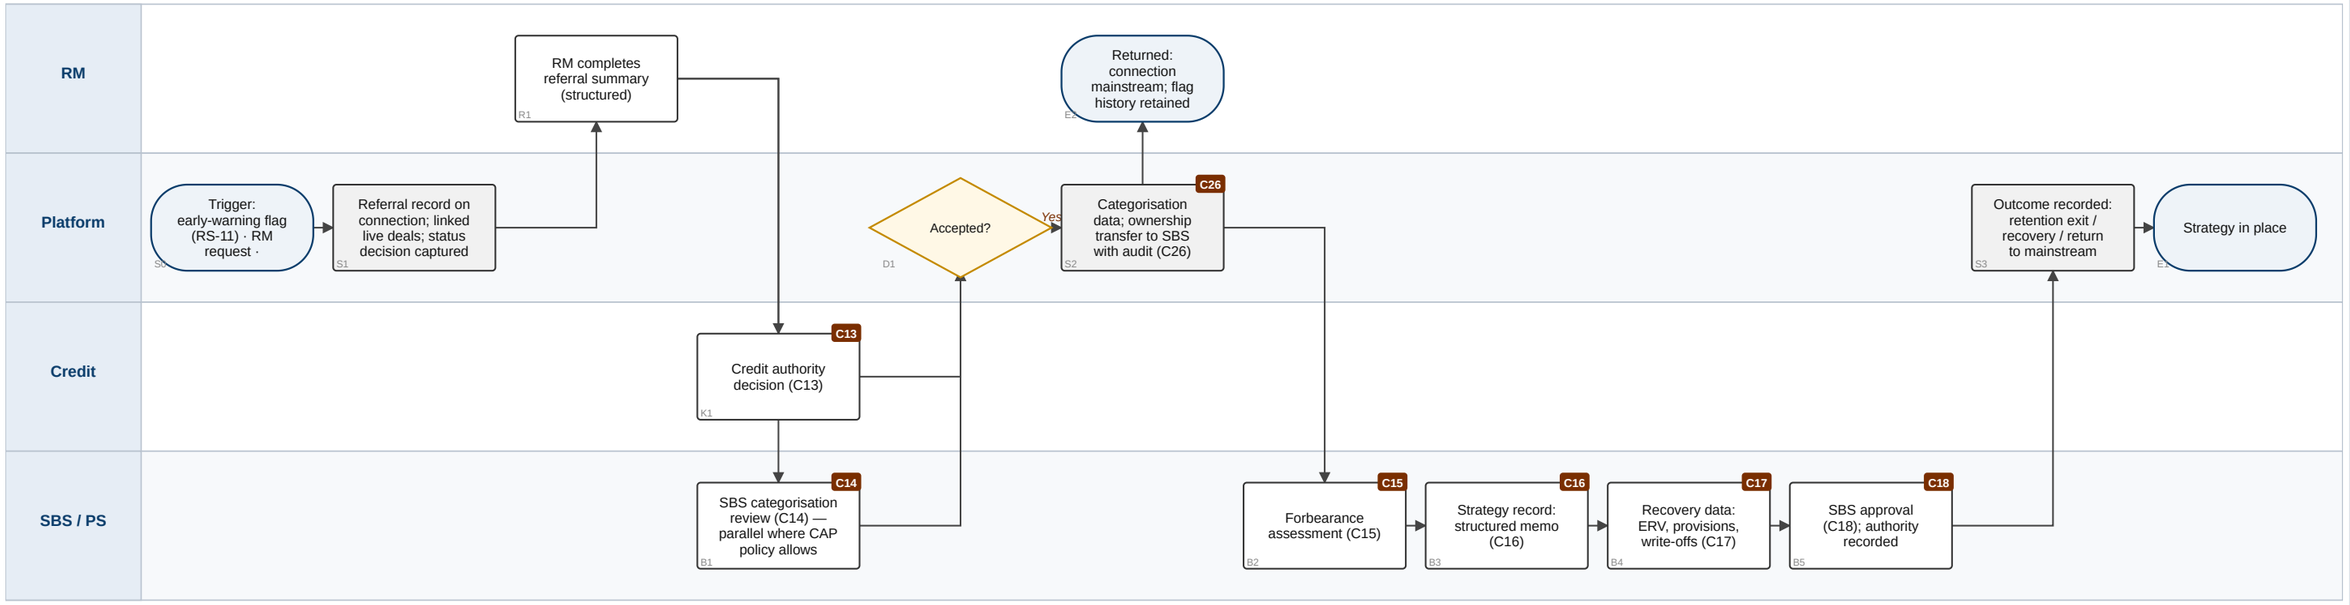

Design notes


- Referral and strategy become one pattern with a referral record, not two deal types.
- Credit and SBS review in parallel where CAP policy permits (PQ-002); sequential otherwise. Either way, the memo is read once from a shared record.
- All regulatory fields (F10, F11) captured in structured, validated form at the same steps as today.

L4 step table

ID	Lane	Step	Type	Control	Wait	Note / rule reference
S0	Platform	Trigger: early-warning flag (RS-11) · RM request · in-flight referral (EX-D)	Start			
S1	Platform	Referral record on connection; linked live deals; status decision captured (hold / continue / decline)	Platform			Record, not file transfer
R1	RM	RM completes referral summary (structured)	Manual			
K1	Credit	Credit authority decision (C13)	Manual	C13		
B1	SBS / PS	SBS categorisation review (C14) — parallel where CAP policy allows (PQ-002)	Manual	C14		
D1	Platform	Accepted?	Decision			
E2	RM	Returned: connection mainstream; flag history retained	End			
S2	Platform	Categorisation data; ownership transfer to SBS with audit (C26)	Platform	C26		Replaces mass officer-code batch for this use
B2	SBS / PS	Forbearance assessment (C15)	Manual	C15		Regulatory; protected F10
B3	SBS / PS	Strategy record: structured memo (C16)	Manual	C16		On platform (OP-20)
B4	SBS / PS	Recovery data: ERV, provisions, write-offs (C17)	Manual	C17		Validation rules on entry; protected F11
B5	SBS / PS	SBS approval (C18); authority recorded	Manual	C18		
S3	Platform	Outcome recorded: retention exit / recovery / return to mainstream	Platform			
E1	Platform	Strategy in place	End			

TB-EXA · EX-A Decline, appeal, refer

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-02, DP-07	EX-01 (straw-man)	OP-08	Customer · RM · Platform · Credit

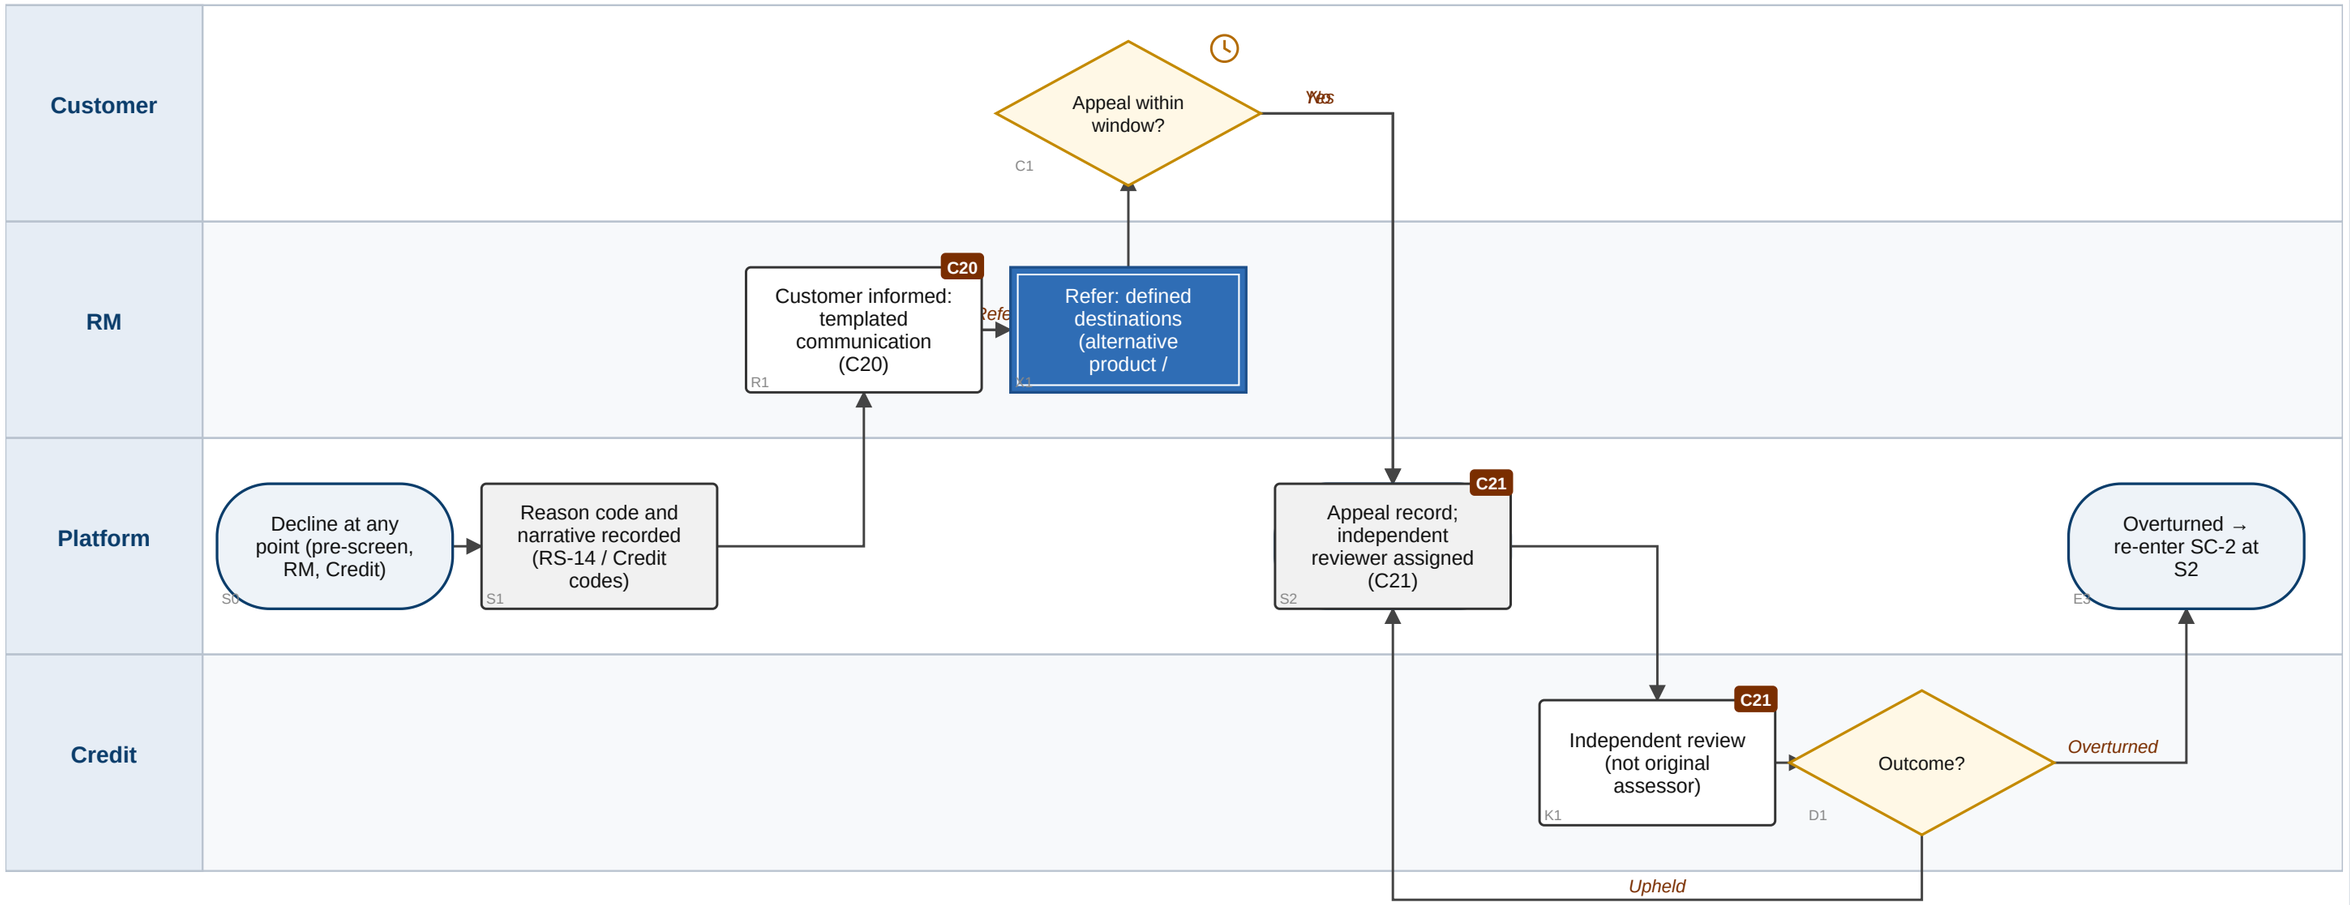

Design notes

- Every decline has a reason code; every appeal has an independent reviewer; “refer” has defined destinations.


L4 step table

ID	Lane	Step	Type	Control	Wait	Note / rule reference
S0	Platform	Decline at any point (pre-screen, RM, Credit)	Start			
S1	Platform	Reason code and narrative recorded (RS-14 / Credit codes)	Platform			Feeds RR-07
R1	RM	Customer informed: templated communication (C20)	Manual	C20		
C1	Customer	Appeal within window?	Decision		●	
E1	Platform	Closed: declined	End			
S2	Platform	Appeal record; independent reviewer assigned (C21)	Platform	C21		
K1	Credit	Independent review (not original assessor)	Manual	C21		
D1	Credit	Outcome?	Decision			
E3	Platform	Overturned → re-enter SC-2 at S2	End			

X1	RM	Refer: defined destinations (alternative product / specialist)	Sub-process			

TB-EXB · EX-B Structured deferral (bounded)

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-04, DP-06, DP-07	EX-02 (straw-man); loop on every *-2 map	OP-17, OP-18	Customer · RM · Platform · Credit

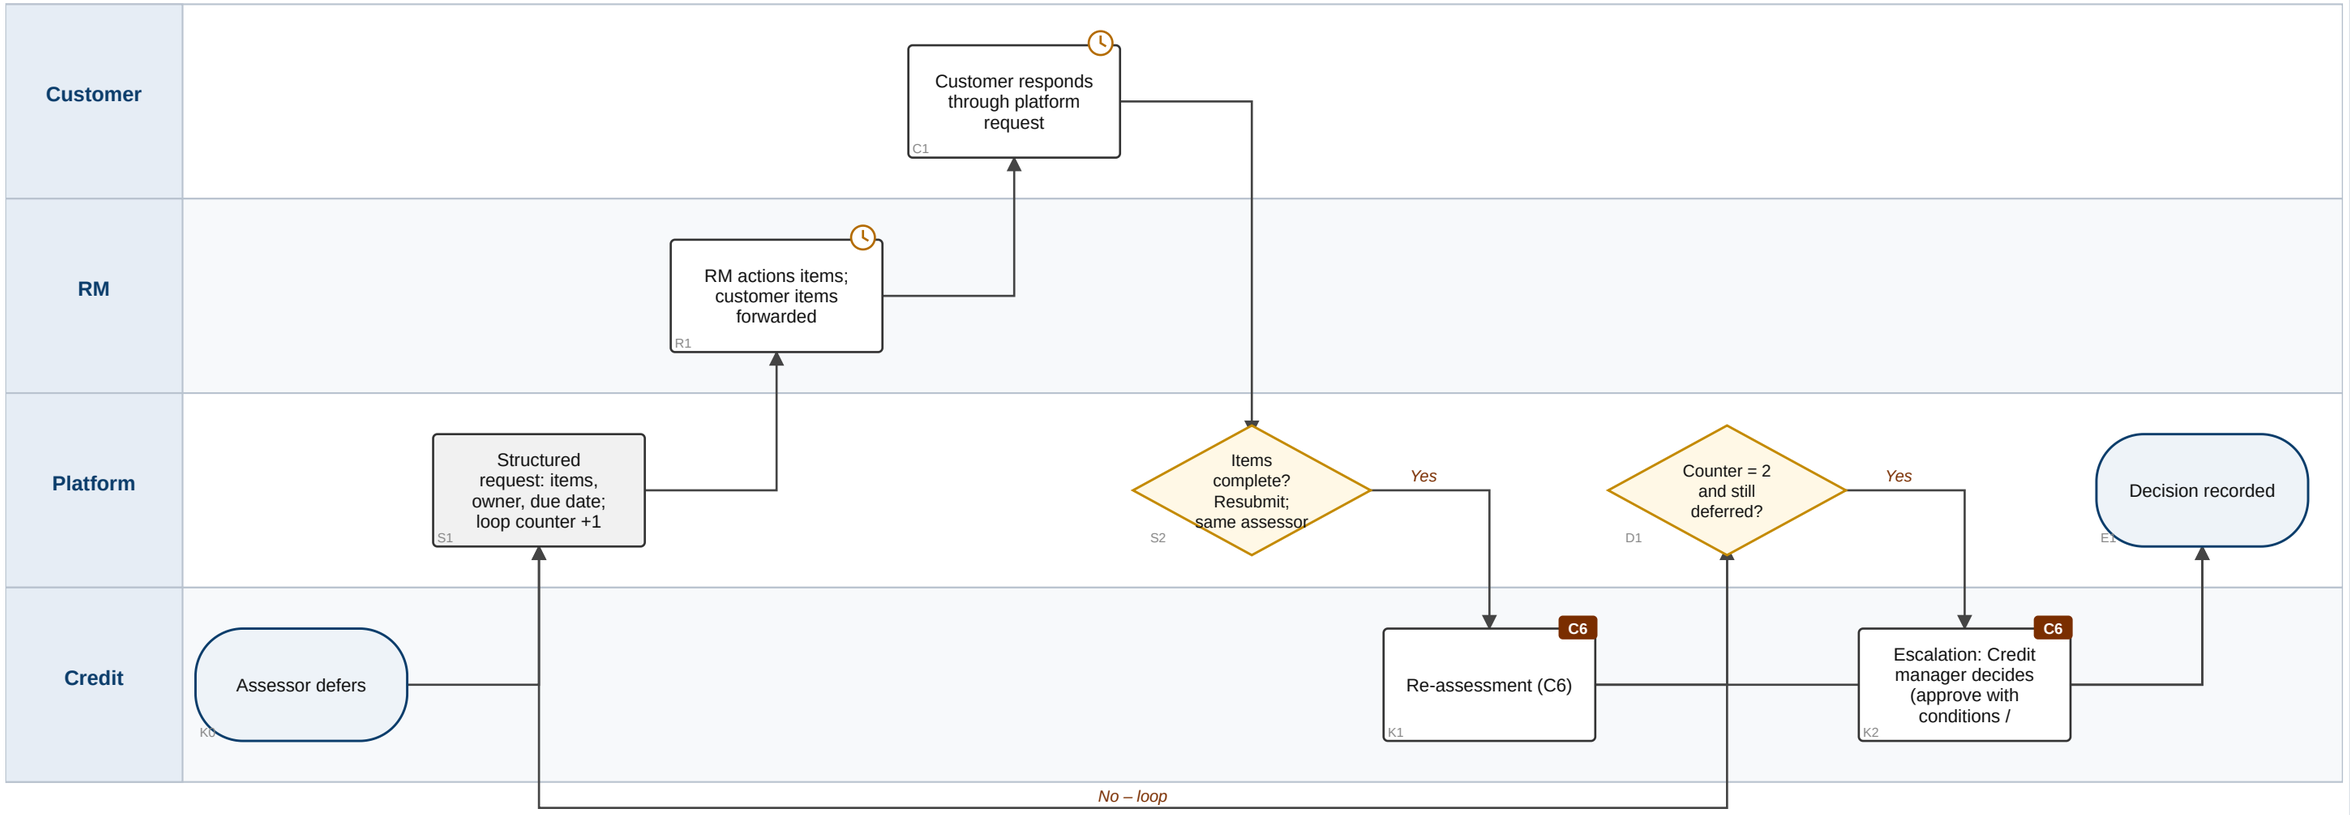

Design notes


- Maximum two loops before escalation; every loop measured (R2, R3).
- The structured request is the data that improves RS-04 over time: items requested most often become submission-standard items.

L4 step table

ID	Lane	Step	Type	Control	Wait	Note / rule reference
K0	Credit	Assessor defers	Start			
S1	Platform	Structured request: items, owner, due date; loop counter +1 (RS-09)	Platform			Replaces free-text comment
R1	RM	RM actions items; customer items forwarded	Manual		●	
C1	Customer	Customer responds through platform request	Manual		●	
S2	Platform	Items complete? Resubmit; same assessor retained	Decision			
K1	Credit	Re-assessment (C6)	Manual	C6		
D1	Platform	Counter = 2 and still deferred?	Decision			
K2	Credit	Escalation: Credit manager decides (approve with conditions / decline / one further loop with reason)	Manual	C6		
E1	Platform	Decision recorded	End			

TB-EXC · EX-C Post-approval change (materiality)

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-01, DP-02, DP-07	EX-03 (straw-man)	OP-09	Customer · RM · Platform · Credit

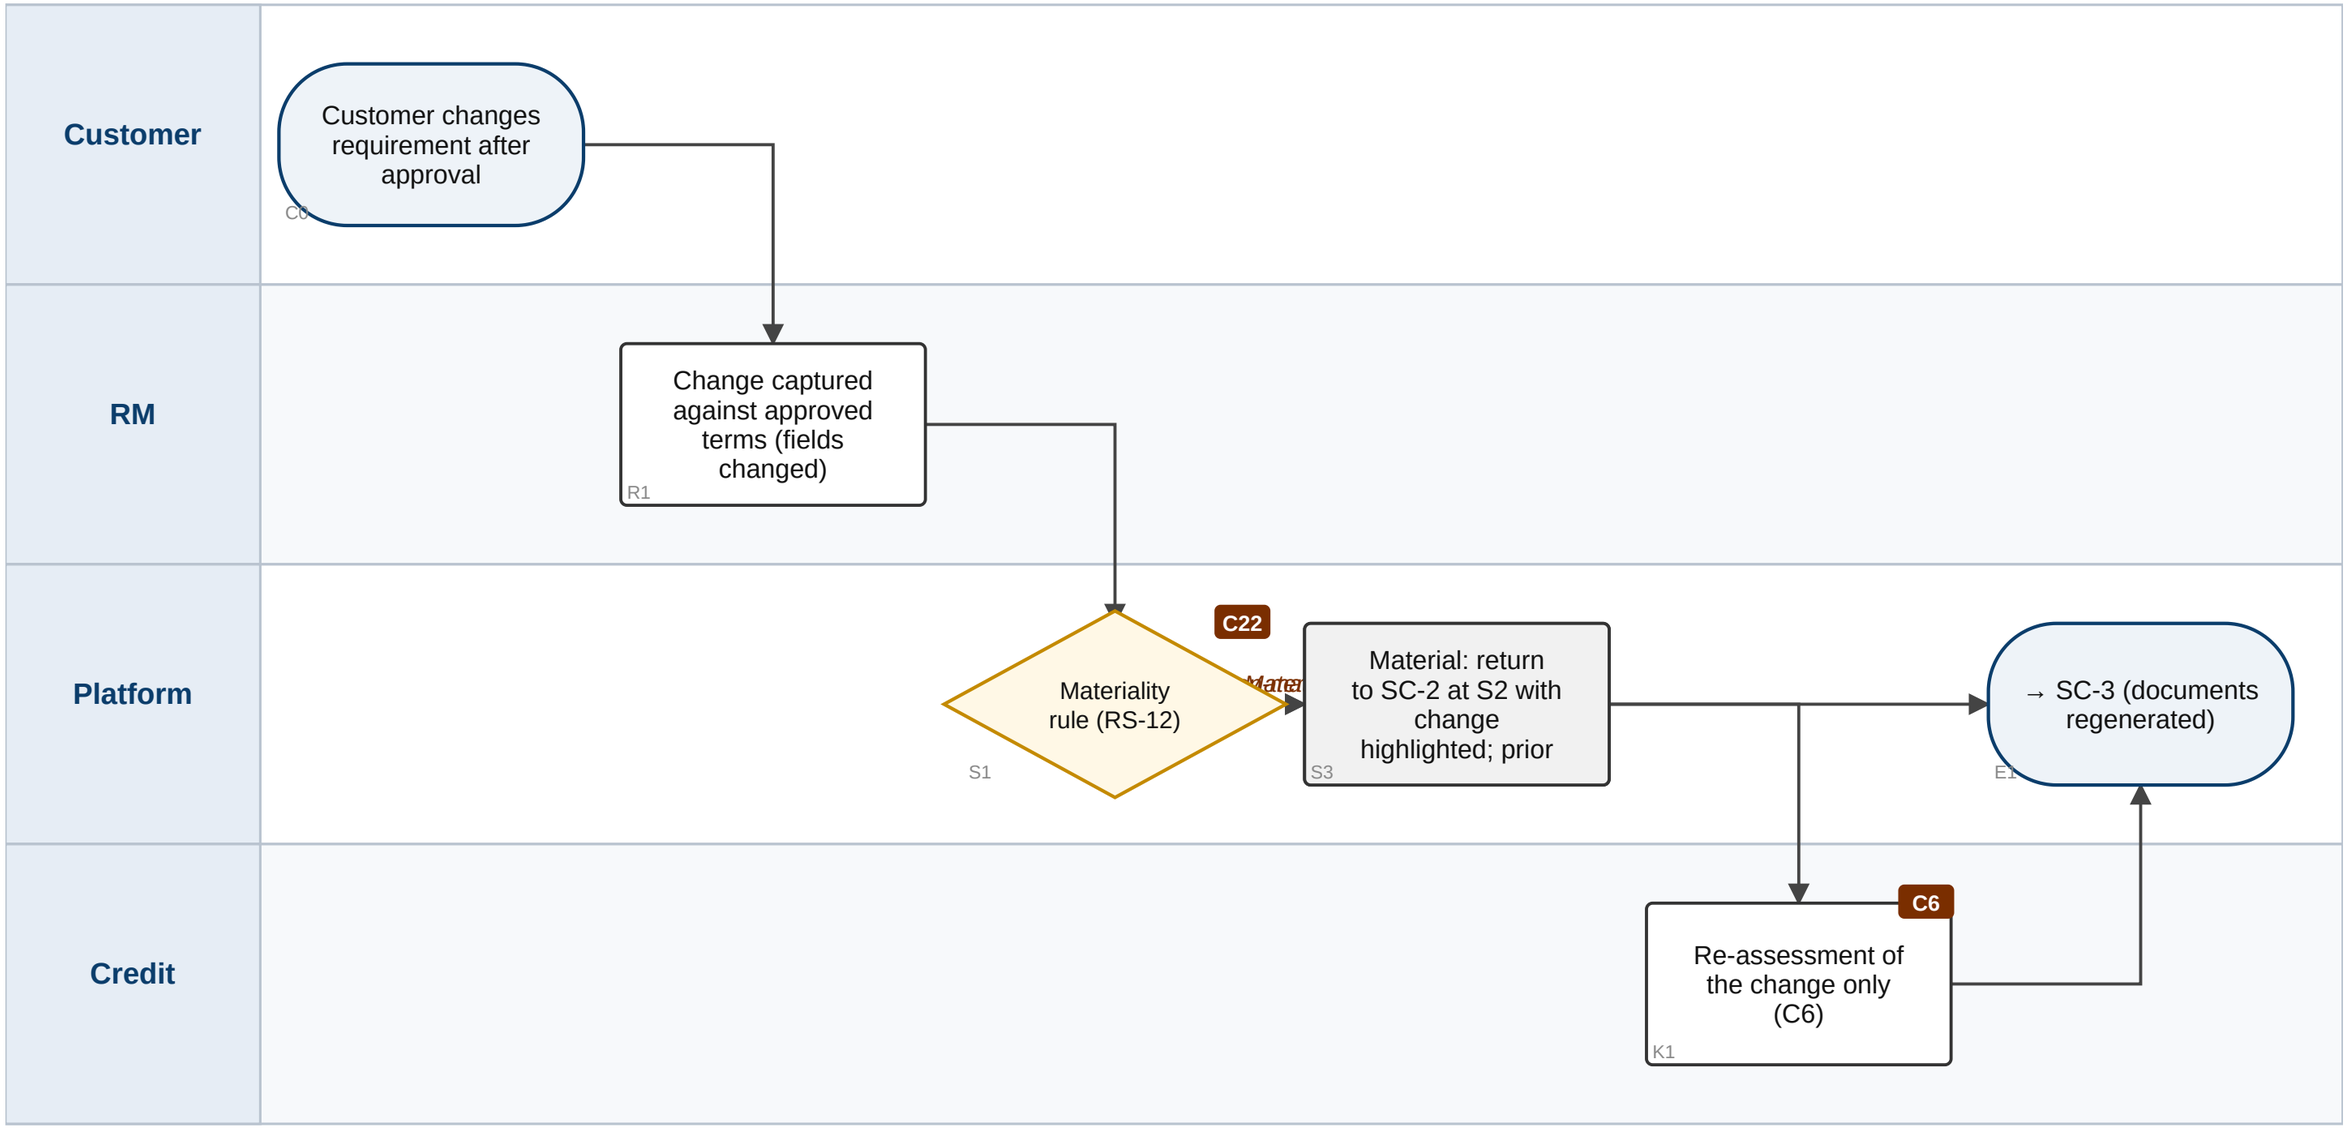

Design notes

- C22 becomes a rule (RS-12) rather than an undefined practice; re-assessment is of the change, not the deal.


L4 step table

ID	Lane	Step	Type	Control	Wait	Note / rule reference
C0	Customer	Customer changes requirement after approval	Start			

R1	RM	Change captured against approved terms (fields changed)	Manual			
S1	Platform	Materiality rule (RS-12)	Decision	C22		
S2	Platform	Non-material: terms and documents regenerated; approval stands; change logged	Platform			
S3	Platform	Material: return to SC-2 at S2 with change highlighted; prior assessor retained	Platform			
K1	Credit	Re-assessment of the change only (C6)	Manual	C6		
E1	Platform	→ SC-3 (documents regenerated)	End			

TB-EXE · EX-E Graduated staleness control

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-03, DP-04, DP-07	3-month reset on *-3 maps	OP-16, OP-30 (interim)	Customer · RM · Platform · Credit

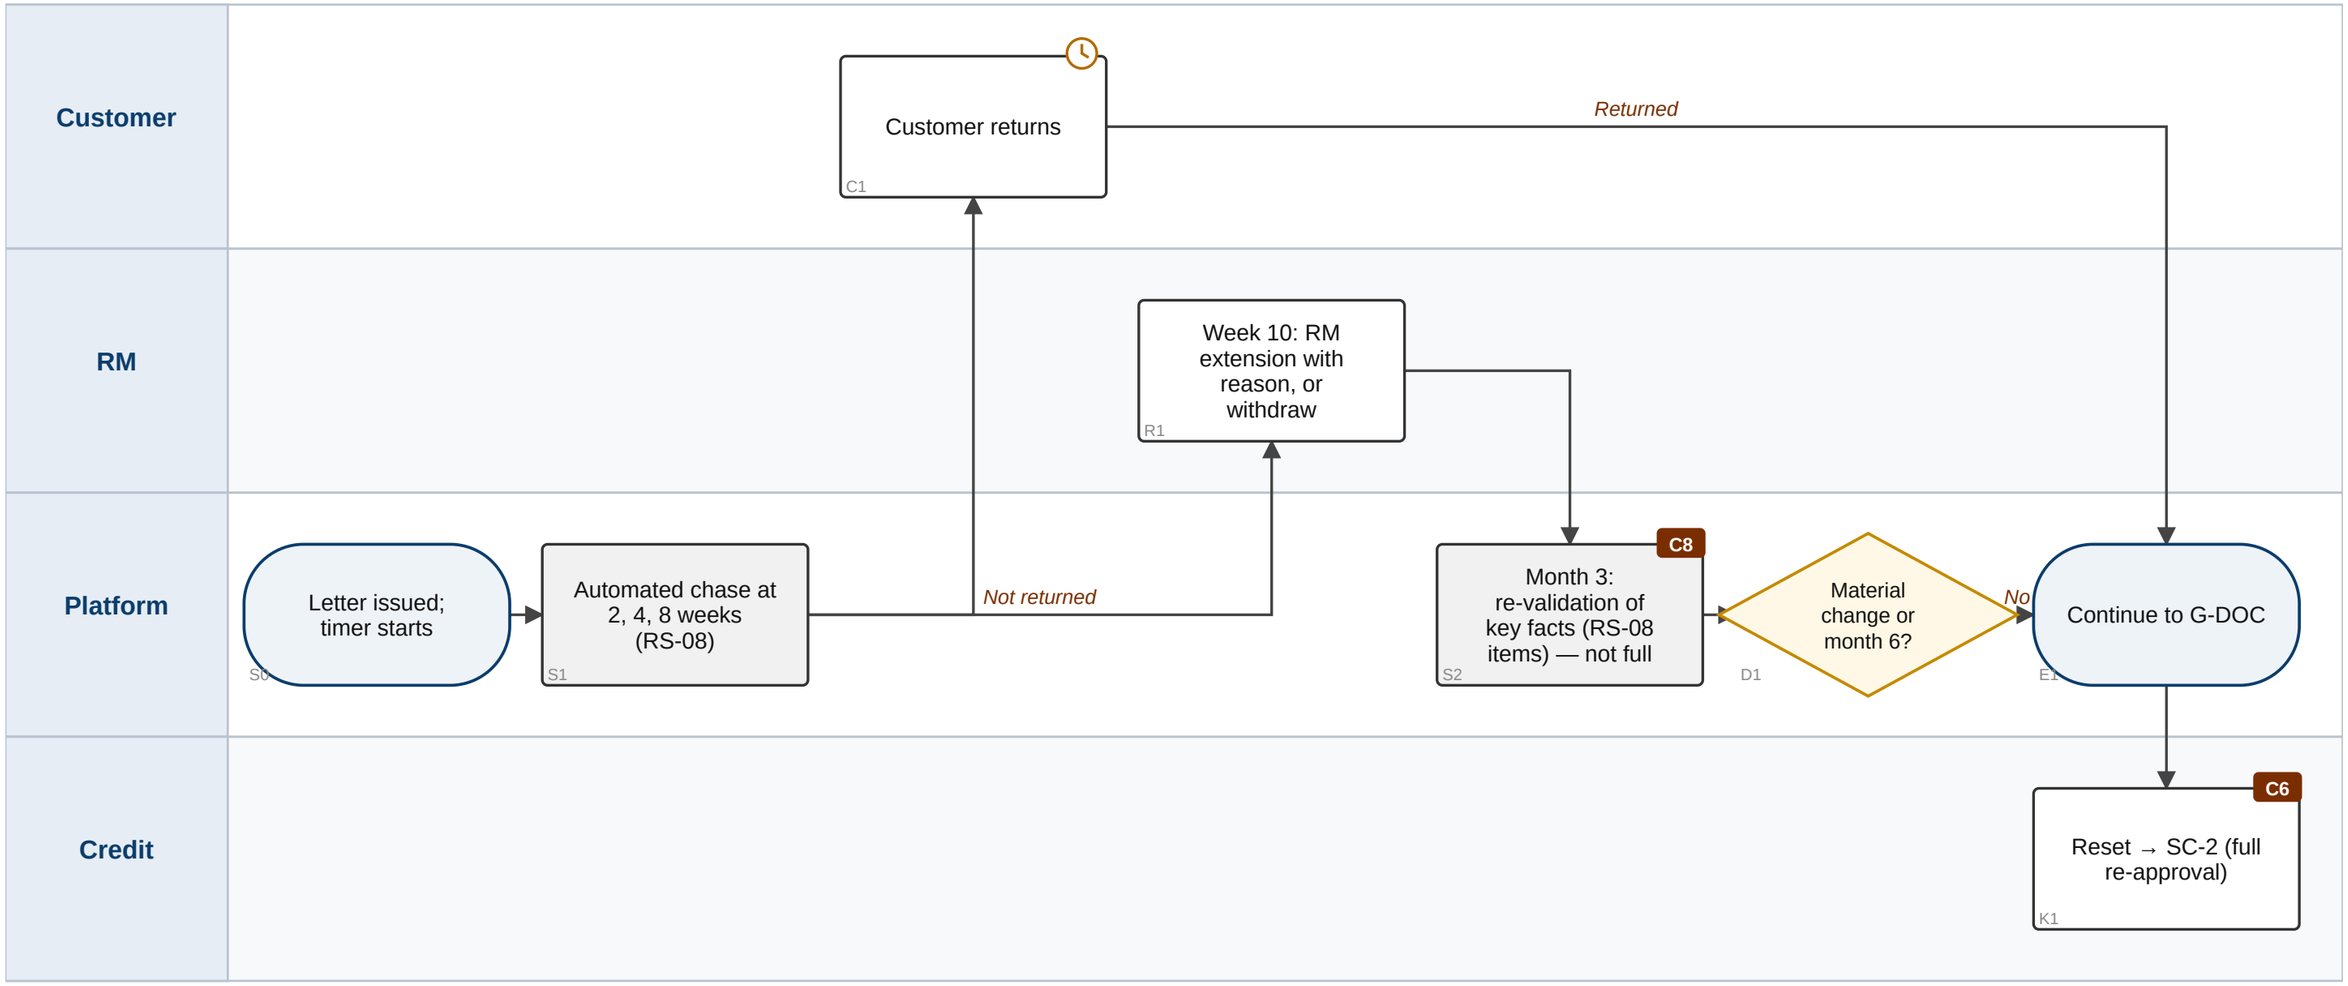

Design notes

- Equivalence case CE-002: the as-is control (hard reset at 3 months) is replaced by chase evidence, an RM extension with reason, a re-validation of the facts the approval depended on, and a reset only on material change or at 6 months. Second line signs the item list for re-validation.

L4 step table


ID	Lane	Step	Type	Control	Wait	Note / rule reference
S0	Platform	Letter issued; timer starts	Start			
S1	Platform	Automated chase at 2, 4, 8 weeks (RS-08)	Platform			
C1	Customer	Customer returns	Manual		●	
R1	RM	Week 10: RM extension with reason, or withdraw	Manual			
S2	Platform	Month 3: re-validation of key facts (RS-08 items) — not full re-approval	Platform	C8		CE-002

D1	Platform	Material change or month 6?	Decision			
E1	Platform	Continue to G-DOC	End			
K1	Credit	Reset → SC-2 (full re-approval)	Manual	C6		

3. Pattern compositions

TB-P1 · P1 New or increased lending · composition

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-01, DP-10	NM-1/2/3, SL-1/2/3	—	Pattern

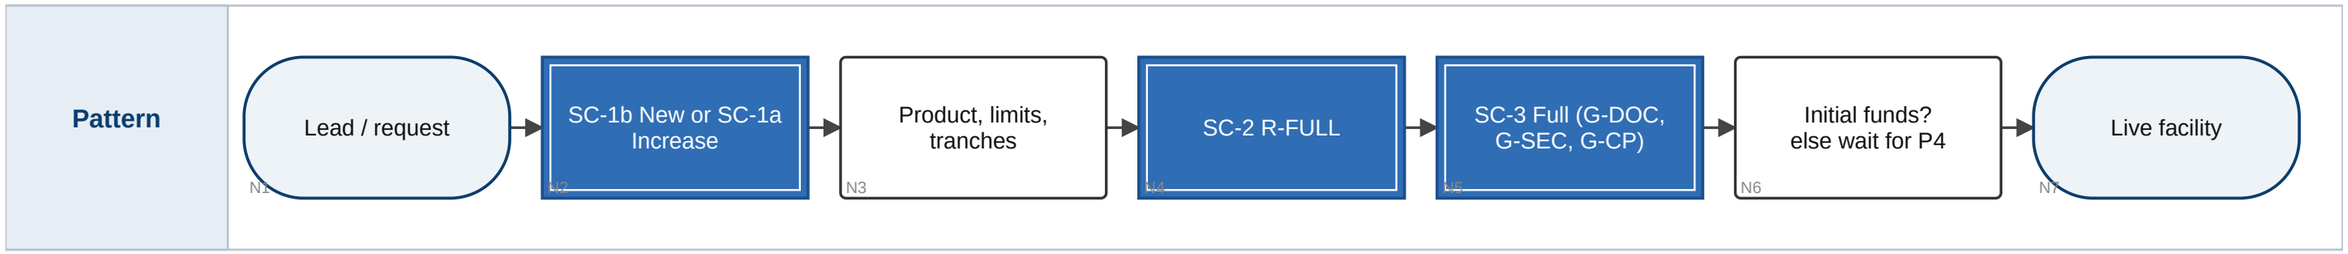


Design notes

- R-FULL only in Release 1; Increase fast-track is a later candidate.
- Shadow limit with no initial drawdown ends after G-DOC and is drawn via P4.

TB-P2 · P2 Renewal · composition

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-01, DP-10	RN-1/2/3	—	Pattern

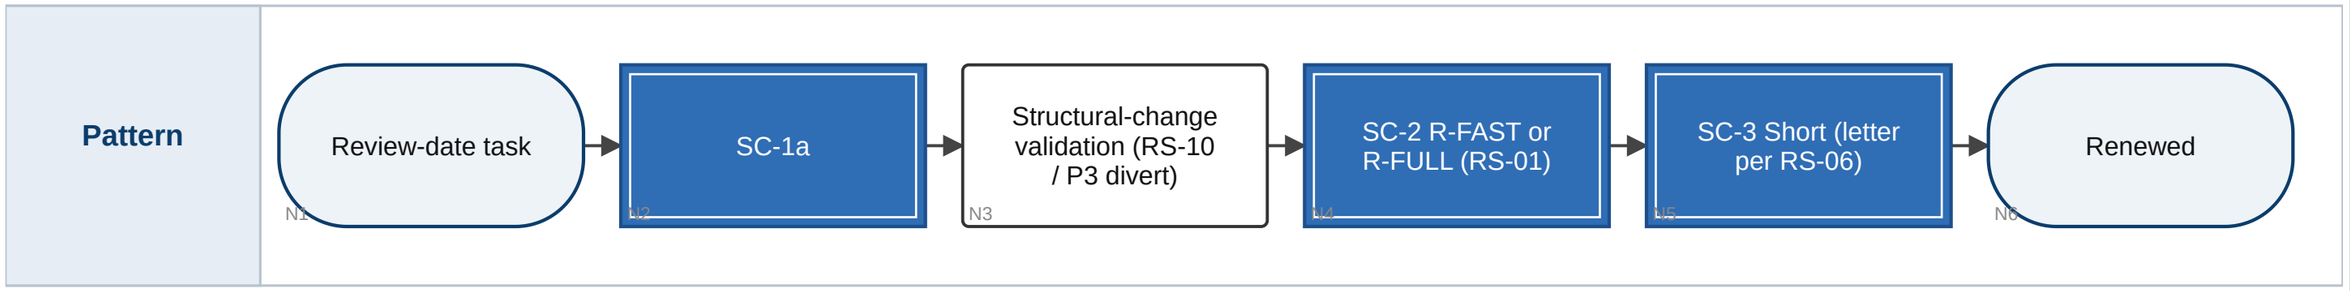


Design notes

- Eligibility (RS-01) and early-warning exclusion decide the route; EPR is a parameter with a counter.
- Any structural change diverts to P3 before SC-2.

TB-P3 · P3 Servicing change · composition

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-01, DP-10	VA-1/2/3, RF-1, EX-03	—	Pattern

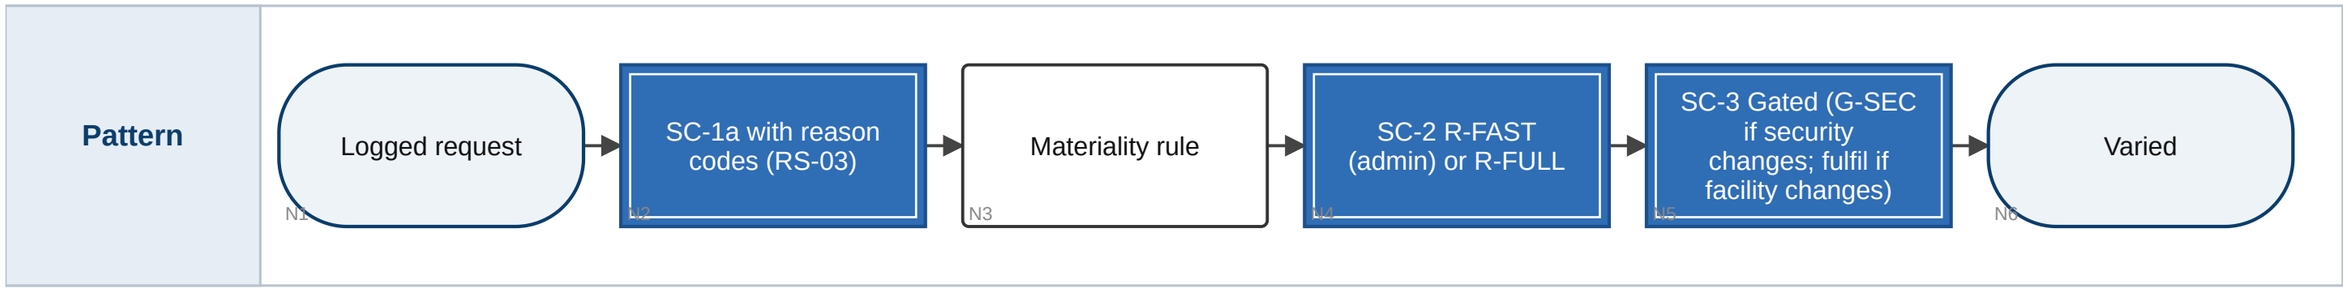


Design notes

- Removal reason routes to TB-P3R.
- EX-C enters here from any pattern.

TB-P4 · P4 Pre-approved drawdown · composition

Principles applied	Replaces (1.2)	Opportunities (1.10)	Lanes
DP-01, DP-10	SR-1/2, SD-1/2	—	Pattern

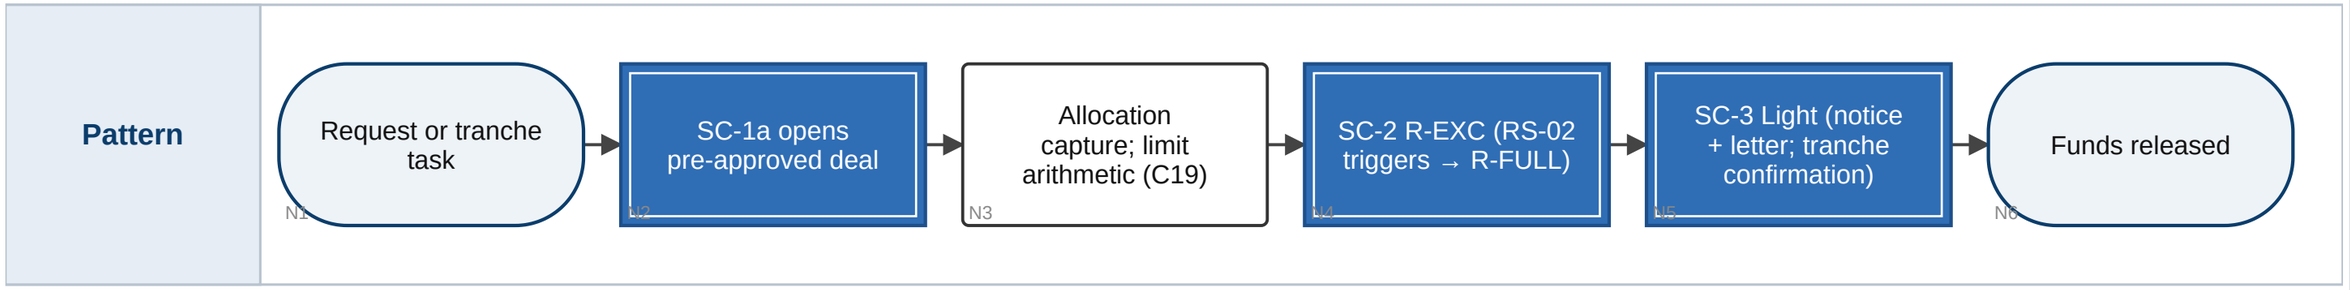

Design notes

- Repayment schedule regenerated per tranche by the system.
- Off-platform letters end: tranche confirmation and reduced-limit notice are templates.

4. Disposition register · every as-is step

Rows are the 62 step rows of the deal type × stage matrix (1.3 §2). Each is marked against the to-be. Rows marked Retained are still human steps; most gain a rule, evidence or SLA.

Row	As-is step (1.3)	Disposition	To-be location	Reason	Principle	Control effect
1.01	Trigger / lead received	**Automated**	SC-1 S1	System event replaces report / phone / email	DP-05	—
1.02	Login	**Eliminated**	—	SSO; no separate login	DP-05	—
1.03	View landing page	**Consolidated**	Work queue	Landing page becomes the task queue	DP-04, DP-05	—
1.04	Search for customer	**Eliminated**	SC-1a S2	Trigger identifies the customer; search only on SC-1b	DP-05	C1 retained in SC-1b
1.05	Customer located	**Automated**	SC-1a S2	Loaded with the event	DP-05	—
1.06	Record customer details (new)	**Automated**	SC-1b S3	Created or matched via CIF	DP-09	C1 strengthened
1.07	Retrieve customer details / identify contact	**Automated**	SC-1a S2	Parties loaded; completeness checked	DP-05, DP-09	C1
1.08	Any additional parties?	**Automated**	SC-1a S4	Party completeness rule	DP-02	C1 strengthened
1.09	Lending or deposit?	**Retained**	SC-1 (per SD-03)	Deposit status on connection or CRM	DP-09	—
1.10	Create opportunity	**Eliminated**	—	Opportunity is a deal status, not an object	DP-05	—
1.11	Select product(s)	**Retained**	SC-1b R2 / P1	Retained; tranche schedule captured as data	DP-09	—
1.12	Passes initial overview?	**Automated**	SC-1b S2	Rule with recorded outcome and reason	DP-02	C0 strengthened
1.13	Contact customer to progress	**Retained**	SC-1b R1	Retained with SLA from lead	DP-04	—
1.14	Details of existing deal pulled through	**Automated**	SC-1a S2	Loaded with the event	DP-05	—
1.15	Provide existing product balances	**Automated**	SC-1a S2	Integration; refreshed at submission	DP-09	—
1.16	Create credit application / select deal type	**Eliminated**	SC-1a S5	Pattern set by trigger; deal type a parameter	DP-01	—
1.17	Add / edit products within pre-approved limit	**Automated**	SC-2 S1 (R-EXC)	Limit arithmetic enforced	DP-02	C19 strengthened
2.01	Convert / progress deal	**Eliminated**	—	No separate conversion; deal exists from SC-1	DP-05	—
2.02	Pull through existing deal; balances	**Automated**	SC-1a S2	As 1.14 / 1.15	DP-05	—
2.03	Customer analysis	**Retained**	SC-2 R1 / R2	Content per RS-04 by route	DP-01	C2
2.04	Credit analytics (C2)	**Retained**	SC-2 R2; integrated (OP-19)	“If required” replaced by RS-04	DP-01, DP-02	C2 strengthened
2.05	Customer provides additional information	**Automated**	EX-B	Structured request on platform	DP-06	—
2.06	Update system incl. balances	**Automated**	SC-2	Continuous; no separate step	DP-09	—
2.07	Progress? (RM go / no-go)	**Retained**	SC-2	Recorded decision with reason (withdraw / proceed)	DP-02	—
2.08	Validate the deal (C3)	**Automated**	SC-2 S2	Submission standard as system rules	DP-02, DP-07	C3 strengthened
2.09	Check facility letter / agreement docs (C4)	**Automated**	SC-3 S3	Reconciliation of returned letter to terms; letter generated from terms	DP-06	C4 → reconciliation
2.10	Within delegated authority? (C5)	**Automated**	SC-2 S3	Automated determination; level recorded	DP-02	C5 strengthened
2.11	Deal transferred to Credit	**Automated**	SC-2 S4	Queue task with SLA	DP-04	—
2.12	Deal is assessed (C6)	**Retained**	SC-2 K1	Retained for R-FULL outside authority; sampling for R-FAST	DP-03	C6; CE-001
2.13	Client in financial distress? (C7)	**Consolidated**	SC-1a S3 + SC-2 K1	Flag at start; judgement retained in assessment	DP-08	C7 relocated
2.14	Credit decision	**Retained**	SC-2 D3 / R3	Retained; recorded with authority	DP-02	C6
2.15	Deferred – further info loop	**Retained**	EX-B	Bounded, structured, measured	DP-07	—
2.16	Declined → EX-01	**Retained**	EX-A	Reason codes; appeal; refer	DP-07	C20, C21
2.17	Credit approved within DA	**Retained**	SC-2 R3	Retained with evidence	DP-02	C5
2.18	Update with approved decision	**Automated**	SC-2 S5	Terms become document source	DP-06	—
2.19	Transfer to SBS; categorisation (C14)	**Retained**	P5 B1	Referral record; parallel where policy allows	DP-08	C14; PQ-002
2.20	Forbearance; team transfer; officer reassignment (C15)	**Retained**	P5 B2, S2	Retained; ownership transfer with audit	DP-09	C15, C26
2.21	CAP Strategy memo; recovery updates; SBS approval	**Retained**	P5 B3–B5	Structured memo; validated fields	DP-06, DP-09	C16, C17, C18
2.22	In-flight CAP referral	**Retained**	EX-D → P5	Referral record; live-deal status explicit	DP-08	C7
3.01	Trigger facility letter(s)	**Automated**	SC-3 S1	Generated from terms; letter-required rule	DP-06	—
3.02	RM advises Lending Services to prepare security	**Automated**	SC-3 S4	Instruction generated from conditions when RS-07 applies	DP-06	C23 strengthened
3.03	FAL created and copy stored	**Automated**	SC-3 S1	System object with status	DP-06	—
3.04	FAL sent by post / secure email (manual)	**Automated**	SC-3 S2	E-delivery; wet-ink exception	DP-06	—

3.05	Customer needs to sign?	**Automated**	SC-3 S1 (RS-06)	Rule, not judgement	DP-02	—
3.06	Customer signs and returns	**Retained**	SC-3 C1	E-signature; tracked	DP-06	—
3.07	3-month unreturned → pre-credit	**Retained**	EX-E	Graduated control	DP-03, DP-07	CE-002
3.08	FAL checked (C8)	**Automated**	SC-3 S3	Reconciliation automated for e-signed; manual for wet-ink	DP-06	C8
3.09	FAL updated as complete	**Automated**	SC-3 S3	Gate G-DOC	DP-04	—
3.10	All pre-conditions met (C9)	**Automated**	SC-3 S5 / R1	Itemised, evidenced	DP-02	C9 strengthened
3.11	Lending Services mark security complete (C10)	**Retained**	SC-3 G2	Retained with registration evidence; queue	DP-04	C10
3.12	BLP marked ready for fulfilment	**Automated**	SC-3 D1	Gates evaluated by system	DP-04	—
3.13	Facility change required? / initial funds?	**Automated**	SC-3 variants	Rule by pattern and reason	DP-01	—
3.14	Message sent to fulfilment team	**Automated**	SC-3 S6	Task with SLA	DP-04	—
3.15	Facility / funding fulfilled (C11)	**Retained**	SC-3 F1	Retained; terms flow from deal (integration later)	DP-10	C11
3.16	RM advised; BLP updated	**Automated**	SC-3 S7	Notification and timestamps	DP-09	—
3.17	Repay balance; release security (C12)	**Retained**	TB-P3R	Sequence corrected; shared-security check	DP-03	C12, C10
4.01	Change after approval → re-process	**Retained**	EX-C	Materiality rule	DP-07	C22 → RS-12
4.02	EPR caps	**Automated**	P2 (RS-10)	Counter enforced	DP-02	—
4.03	Renewal: only dates change	**Automated**	P2 structural validation	System validates; divert to P3	DP-01	—
4.04	Skip CDQ → PDQ; DCA 5	**Automated**	SC-2 R-EXC (RS-02)	Rule-based route	DP-01	C5
4.05	Auto-reoriginate at 90 days (batch)	**Retained**	Workflow timer (OP-12)	Warning at 60 / 80 days; reset with reason	DP-04	C24
4.06	Restructure flag	**Retained**	P1 parameter	Retained	—	—

5. Design decision records and dependencies

5.1 Design decisions embodied in these maps

DDR	Decision	Principles	Evidence	Control / data	Fit-gap (2.7)
DDR-001	Renewals meeting RS-01 approved within line authority without Credit transfer (R-FAST), subject to PQ-001 and CE-001	DP-01, DP-02, DP-03, DP-08	PP-09; A1 confirmed; A2 cohort; SR/SD precedent	CE-001; F06 grade refresh rule; F07 authority	Configure if rule routing native; else Custom
DDR-002	Deal start is one component with two entry variants; opportunity object retired	DP-05, DP-09	1.3 stage 1 100% common; PP-03, PP-06	C0 → rule; C1 strengthened	Configure
DDR-003	Delegated-authority determination automated with recorded level and rule version; manual override with reason	DP-02	PP-15; E2	C5 strengthened; F07	Configure (rules) / Custom (engine depth)
DDR-004	Facility letters generated from approved terms, e-delivered, e-signed, reconciled; off-platform letters end	DP-06, DP-09	PP-23, PP-25; C2, D2, D3	C4 → reconciliation; C8; F13 captured	Configure / partner integration (G1 decision 3)
DDR-005	3-month reset replaced by graduated staleness control (EX-E)	DP-03, DP-07	PP-24; R4	CE-002	Configure (timers)
DDR-006	Deferral bounded at two loops with escalation; structured request; same assessor	DP-07, DP-04	PP-13, PP-14; C1	RS-09; measured R2	Configure
DDR-007	Early-warning flag evaluated at deal start; excludes fast-track; prompts P5	DP-08	PP-34, PP-17; RC-08	C7 relocated; RS-11	Configure (if indicators available) / Gap (data)
DDR-008	Hand-offs become queue tasks with SLAs; messages and reports as triggers end	DP-04	PP-16, PP-29, PP-39	— (ownership in 2.9)	Configure
DDR-009	Variation routed by reason taxonomy and materiality rule; security gate only when security changes	DP-01, DP-02	PP-18, PP-28; A4	RS-03, RS-07; CE-003 (admin route)	Configure
DDR-010	Removal sequence: physical release before system release; shared-security check by rule	DP-03	PP-30; RF-2 TBC	C10, C12 strengthened	Configure
DDR-011	Referral is a record on the connection; Credit and SBS review in parallel where CAP policy permits	DP-08	PP-21; RC-08	PQ-002; C13, C14	Configure
DDR-012	Three deal types retired; two un-typed journeys housed in P3 and P4; type is a parameter	DP-01, DP-09	1.3 §5; B3	F03 mapping table	Configure

5.2 Items the maps depend on

Ref	Item	Owner	Needed by	If not resolved
PQ-001	Renewal authority: may unchanged, eligible renewals be approved within RM / line authority?	Head of Credit Risk Policy	W10	R-FAST designed but not activated; P2 runs R-FULL with automated DA (still removes PP-15)
PQ-002	CAP policy: may SBS categorise in parallel with Credit authority for defined triggers?	Head of Credit Risk Policy; Head of SBS	W10	P5 sequential; T8 benefit reduced
CE-001	Equivalence for R-FAST bypass of C6: automated DA with evidence; eligibility rule; Credit sampling; grade staleness rule	Second-line Risk	W11	As PQ-001
CE-002	Equivalence for EX-E replacing the 3-month reset	Second-line Risk	W11	Reset retained at 3 months with chase evidence; OP-16 value lost
CE-003	Equivalence for administrative variations approved without Credit (R-FAST in P3)	Second-line Risk	W11	P3 runs R-FULL for all; OP-02 value lost
G1-D3	Document generation, e-delivery, e-signature in Release 1	Programme Director	W10	SC-3 S1–S3 on custom list or interim OP-30

5.3 Review and sign-off route

Week	Review	Participants	Output
9	Working-group walkthrough: SC-1, SC-2, P2, P3	WG Renewal, WG Servicing, Credit Managers	Corrections; RS-01, RS-03 content started (2.4)
10	Working-group walkthrough: SC-3, P1, P4, P5, exception paths	WG New, WG Pre-approved, WG Distressed, Lending Services, Fulfilment	Corrections; interim release to Programme (B-04)
11	Design preview with senior RMs, Credit, Ops heads (C-11)	Front line	Workability confirmed or changes
12	Design Authority sitting	Design Authority	v1.0 signed with CE and PQ status recorded
